RESEARCH FACILITIES DEVELOPMENT PROGRESS REPORT

I. BASIC INFORMATION	
1. Project Title	***Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus***
2. Proponent/s	
a. Implementing Agency i. Name: ii. Location: iii. Email Address: iv. Landline Number:	Partido State University San Juan Bautista St., Goa, Camarines Sur 4422 Philippines op@parsu.edu.ph (054) 871-2090
b. Agency Head i. Name: ii. Designation:	Zarcedo, Arnel Bono SUC President III
c. Project Leader: v. Name and Signature: ii. Position/Designation: iii. Office/Department: iv. E-mail Address: v. Mobile Number: vi. Landline Number:	Sadol, Joel Paulite Associate Professor II joel.sadol@parsu.edu.ph
d. Co-Project Leader: v. Name and Signature: ii. Position/Designation: iii. Office/Department: iv. E-mail Address: v. Mobile Number: vi. Landline Number:	Lorio, Jenny Punto Associate Professor II/College Dean PSU-College of Agribusiness and Community Development (Salogon Campus) jenny.lorio@parsu.edu.ph +639813863814
3. Project Site/s	
a. Province b. City(-ies)/Municipality (-ies) c. Barangay(s) d. Geocode(s) *(lat,long)*	Camarines Sur San Jose Salogon 13.655327989957211, 123.50870833580969 (13° 40' North, 123° 31' East)
4. Project Funding	
Source of Fund:	*Amount (PhP):*
a. DA-BAR/DA-ACEF	Item/s of Support: ■ Facility (F) ☐ Equipment I ☐ Both (F&E)
i. Total Amount Approved	P1,599,474.50
ii. Total Amount Released	P1,599,474.50
iii. Total Amount Disbursed	P820,365.37 (waiting for the report on additional disbursement) As of: April 24, 2024
iv. Unliquidated Balance	P779,109.13
b. Agency Counterpart	Item/s of Support: ☐ Facility (F) ■ Equipment I ☐ Both (F&E)
i. Total Amount Approved	P880,000.00
ii. Total Amount Disbursed	-0-

5. Duration	
a. Date Project Started	06/05/2023
b. Extension Period (if applicable)	06/04/2024 to 09/04/2024
c. Date of Completion	09/04/2024
6. Period Covered by Report	06/04/2024 to 07/20/2024

I. PROJECT DESCRIPTION

1. Rationale/Background

Partido State University – Main Campus had already established the tissue culture facility before with the intension of being research and extension center for abaca species in the Partido District. At the onset of this project, the facility somehow served the purpose. However, it was not sustained the purpose due to change of the university priorities. The apparatuses and equipment of the said facility are assessed that they are still working but outdated. The existing facility must be upgraded and be transferred to other campus of the university with manpower and structure capabilities in order that its intended purpose will be met.

At present, abaca and bamboo in 4th District of Camarines Sur were neglected by the farmers to cultivate but during the previous years they were the priority. The less prioritization of the said commodities happened during the time of massive corn and sugarcane production. The areas devoted for said commodities were allotted for planting corn and sugarcane. Farmers were attracted to convert their areas because of the supports and subsidies given by corn and sugarcane industries.

The project is consistent with RA 10848 specifically on Sec 8. The Fund shall be set aside and released for: (a) the increased productivity of farmers and fisherfolk by providing the necessary credit to farmers and fisherfolk and their cooperatives and associations, and micro and small-scale enterprises, for the acquisition and establishment of production, postharvest, and processing machineries, equipment and facilities, farm inputs and improvement; (b) research and development on agricultural and fishery products of state universities and colleges; and (c) a comprehensive and attractive grant-in-aid program for agriculture, forestry, fisheries, and veterinary medicine education to promote the development of agriculture and fisheries.

One of the campuses of the Partido State University which offers program on agriculture is the Salogon Campus. This campus is the appropriate campus to implement and operate tissue culture facility of the university since tissue culture is under the field of agriculture. The campus has the faculty manpower who are knowledgeable in tissue culture and has an unoccupied building intended for renovation which will adopt to the functional requirements of a tissue culture facility. PSU-Salogon campus have engaged to revitalized the glory of abaca and bamboo industry in Partido District. It has envisioned that the current flooding be addressed by this engagement. Hence, the campus has a project collaboration with PhilFIDA on provision of free abaca seedlings to farmers. PhilFIDA had established an abaca nursery station in the campus and PSU shall be responsible for growing abaca seedlings which will be opted for farmers. PSU on similar project mentioned had also established a nursery station for bamboo. PSU will likewise disperse bamboo seedlings to farmers in the district, as part of its extension project.

There is also a need to organize and inform the farmers who will again cultivate abaca and bamboo in the district and in the Bicol Region in particular. From 3,176 abaca farmers cultivating 5,698 hectares of land (PhilFIDA 5 in DA RFO 5 Bikol Profile & Agri-Performance as of June 21, 2022), there are 479 abaca farmers in total in the municipalities of Tigaon, Sagnay, and Goa in Camarines Sur (PhilFIDA). In these municipalities PhilFIDA and PSU-Salogon started the project on abaca seedling distribution, which includes other municipalities in the district at future date.

2. Facility Description

The upgrading of tissue culture facility in Partido State University at Salogon Campus will be an additional center for production of new and improved species of abaca and bamboo seedlings for Bicolano farmers. The farmers who will engage in cultivation of these commodities have the new source of livelihood.

The facility can be used for instruction in crop science subject with topics in plant tissue culture, in strict observance of laboratory guidelines. The facility can be used for researches of students, faculty, and other researchers in the Region as per request. The tissue culture laboratory facility is where the seedlings of abaca and bamboo that will be dispersed to farmer-beneficiaries as an extension project of PSU-Salogon Campus will be cultured.

3. Farm Level Application

Service/Functionality	Target Clientele	Number of Beneficiaries	Location

1. Availability of new/improved species of abaca and bamboo seedlings	Abaca farmers Bamboo farmers	100 100	4th District, Cam. Sur
2. Research facility for abaca and bamboo tissue culture	Students Faculty Researchers Extensionists	200 10 20 20	ParSU Salogon Campus ParSU Salogon Campus Bicol Region Bicol Region

Abaca and bamboo tissue-cultured seedlings will be grown in its respective nurseries located at Partido State University – Salogon Campus. At one month after transplanting, seedlings will be distributed to abaca farmers identified in collaboration with PhilFIDA in the Campus extension project. Monitoring and research activities will be done to dispersed abaca plants, including the performance of abaca, status of the project and profitability.

Other services of the facility to be identified in the manual of operations for a fee will be made available such as production of seedlings for sale.

II. OBJECTIVES

Objective	% Accomplishment	Remarks (Indicate verifiable indicators)
General Objective To upgrade the tissue culture facility in Partido State University at Salogon Campus		*a. For facilities, indicate the % completion in terms of program of works* *b. For equipment, indicate the number of equipment procured*
Specific Objectives		
1. To renovate unoccupied building of Partido State University at Salogon Campus adoptable to Tissue Culture Facility.	100% completed (See Appendix B.1. Certification on the Percent of Project Completion)	An inspection of the facility was conducted by the PSU Inspection Team last June 3, 2024, on the following: *General Requirements *Site works *Structural Works *Architectural Works *Electrical Works *Plumbing Works *Pest Control Partial Payment was made as of April 24, 2024. The remaining amount to complete payment is on process.
2. To procure new apparatuses and equipment	See Appendix A. PPMP	The procurement of equipment, apparatus and chemical reagents

in replacement of outdated and non-functional apparatuses and equipment of existing tissue culture facility.	for Calendar Year 2024: Projects, Programs and Activities (PAPs)	amounting to P880,000.00 is on process.
3. To establish operational plan for Tissue Culture Facility	See attached Appendix C. Operational Plan for the Tissue Culture Laboratory Facility of Partido State University at Salogon Campus, 2024-2030	The operational plan for the facility was crafted anchored to the RDE agenda of the University and the Salogon Campus. The plan will be presented for comments and inputs by the stakeholders including the farmers, researchers, extensionists, students, the Department of Agriculture through its Municipal Agriculture Offices in nearby localities, Sangguniang Bayan, and others. The operational plan highlights the activities and its benefits to beneficiaries congruent to ACEF's objectives of increasing productivity of farmers. The operational plan comprehensively discussed the technical and financial sustainability strategies to sustain operations and the targets to improving the competitiveness of farmers after the project's completion. Strategies include the following: ✓ Sending the faculty in-charge of the facility to training on its management and operations. ✓ Submit the operational plan for endorsement of Administrative Council and BOR. ✓ Hiring of a laboratory technician who is a graduate of BS in Biology or its allied fields; with one year of related working experience; can perform basic tissue culture laboratory activities and techniques; Laboratory Technician I (SG-6; P17,553.00) ✓ An annual budget allocation from the University Income will be allocated for the operations and maintenance of the Tissue Culture

		Laboratory, subject for approval of the Board of Regents. ✓ Requesting the approval of the BOR for the operation and fund for Tissue Culture. ✓ Assigning a Faculty fellow who will be deloaded with corresponding units tasked to propose RDE projects with realizable results/outcomes.

III. ACCOMPLISHMENTS

1. Summary of Activities

Date	Activities
December 28, 2022	Approval of Memorandum of Agreement, with attached: Certification for Fund Transfer to Partido State University, from the Office of the Secretary * DA-Agreement/Contract No: 02132023-21 *Project Title: Upgrading of Tissue Culture Laboratory Facility in Partido State University-Salogon Campus *Charged against: Agricultural Competitiveness Enhancement Fund (ACEF) (3105002000020000) *Amount: P1,599,474,50 *SARO No. BMB-E-22-0010556 dated November 16, 2022
May 31, 2023	Notice to Proceed and Fund Release: * Project duration: June 5, 2023 to June 4, 2024 *LDDAP-ADA No.: 183-04-007-2023 *Date of Fund Transfer: April 26, 2023 *Date received by PSU OP: July 10, 2023, together with MOA, and Approved Proposal.
July 7, 2023	Letter from the Project Leader to the University President informing PSU of the issuance of Notice to Proceed, Release of Fund, and inception meeting of the PSU Officials and DA-BAR personnel. Received by RND Office: July 7, 2023
July 24, 2023	Request by the Project Leader to DA-BAR for the revision of the frontage of the building to meet aesthetic consideration. Attached: *Letter request to PSU University President as signatory of the request for revision. *Date received by PSU OP: August 18, 2023
September 7, 2023	Approval of request for change in facility design Reference No.: 2023-09-31
September 20, 2023	Purchase Request *PR No.: 23-09027 *Amount: P1,599,474,50
December 13, 2023	Notice of Award to Seven "R" Construction & Supply * Amount: P1,516, 301.08 *Conformed: December 20, 2023
May 22, 2024	Request for extension of project implementation

		*Date of extension requested: June 5, 2024 to December 4, 2024 *Received by DA-BAR-ACEF: June 3, 2024 *Attachments: - Accomplishments - Workplan Schedule - Report of Checks Issued *Period Covered: January-April 2024 * Amount: P820,365.37 - Audited Financial Report *LDDAP No.: JEV No. 23-06-0639 - Subsidiary Ledger *Account Code GL 2 04 01 010 00 SL 2 04 01 010 00 –Tissue Culture Lab. *Payment for the 1st partial billing: P820,365.37 *Balance: P779,109.13
	May 28, 2024	Approval of request for project extension *Reference No. 2024-293 * Approved date of extension: Until September 4, 2024 *Received by PSU Office of the University President: June 18, 2024

2. Incremental Improvement/ Outcomes

Perceived/Potential impact/improvement of the project.
Indicate the qualitative and quantitative changes, increases, and improvements of the services, functionalities, and capacities

Particular*	Before Upgrading/ Establishment	After Upgrading/ Establishment	Remarks
1. Facility Area		6 m x 9 m	As approved See Appendix B.2. Justification on the construction instead of renovation; B.4. Approved Technical Drawings and
2. Number of Equipment		5 – equipment; 42 – chemical reagents; 8 other supplies	Approved proposal; See Appendix A. PPMP for Tissue Culture Laboratory Facility
3. Production Capacity		1,000 seedlings per annum	Initial target for the first 2-3 years of operation
4. Service Coverage Area		4th District of Camarines Sur	Will also be available to other municipalities and provinces in the region, as the operation of the project extends and as by clients.
5. Product Quality		Production of good quality seedlings of abaca, bamboo and other crops,	Target quality of seedlings to be produced. Processes and procedures will be adapted from PhilFIDA

			for abaca, as result of the training that will be attended by the assigned. Technoguides in the tissue culture of bamboo and other crops will be followed.
6. Beneficiaries		Abaca farmers – 100 Bamboo farmers – 100 Students – 200 Faculty – 10 Researchers – 20 Extensionists - 20	Target beneficiaries for the first two years of operation. The number will increase as the operation continues.
7. Training offered		Twice a year	Target for the year. The trainings will be anchored as extension projects of the Campus.
8. Services Offered		2 services	The facility will provide services for culture/propagation of seedlings and as facility for researches of faculty and students.
9. Research Conducted		1 per year	Target research conducted per year as part of the research program in abaca, bamboo, and other crops.
10. Products Offered		Abaca and Bamboo seedlings; Will produce tissue cultured materials for other crops.	Target products to be produced in the laboratory facility.

**Particulars may be added depending on the applicability to your facility. Put N/A to those not applicable to the facility.*

3. Service and Functionalities

List all specific services offered/to be offered by the facility. For training/ seminar/ workshops, specify what specific topics will be offered.
This element will serve as the basis for the post-implementation assessment.

Before Upgrading	Description	Clientele
1. *2.*		
Current/ Target (After Upgrading)	**Description** *Indicate prices and other specific details of the services if applicable*	**Target Clientele**
1. Production of tissue-cultured abaca and bamboo seedling	The facility will focus on tissue culture of abaca and bamboo species. Other crops will be produced in the succeeding years of operation. A fee of least 10% higher of the cost of production of the seedlings will be charged.	Abaca and bamboo farmers in 4th District, Camarines Sur
2. Research facility for students, faculty and researchers	The facility will be used for research projects of PSU faculty, other	Students, faculty and researches in Bicol region.

3. Source of abaca and bamboo seedlings for extension projects	researches of Bicol Region and for thesis of students. The facility will produce abaca and bamboo seedlings for dispersal to farmers in PSU's extension programs/projects.	Faculty extensionists, abaca and bamboo farmers

4. Problems/Issues Encountered and Actions Taken

Indicate constraints and challenges encountered during the project duration and what are the actions taken to address this

Problems/Issues Encountered	Actions Taken
Lengthy processing of required documents for the project. The process of sourcing for a supplier to conformance with the Notice of Award and Contract Agreement took so long (more than six months) from the date the Notice to Proceed and Fund from DA-BAR ACEF was released to Partido State University.	Constant follow-up on the concerned unit of the University.
Uncontrollable factors on the part of suppliers/contractors. It was only in February 26, 2024 that the contractor/Supplier started the facility construction.	Constant coordination with the PPF unit of the University.

IV. SUSTAINABILITY AND PLAN OF ACTIVITIES

Indicate the strategies and action plans for the operations and maintenance of the upgraded facility/equipment. Aside from the financial sustainability, also include the organizational stability in terms of workforce/manpower resources and the technical capability. Plans for the compliance to various regulatory standards should also be discussed.

1. Sustainability Plan

a. Financial Sustainability Plan	*The fund for the continuous operation of the Tissue Culture Facility including its staff will be sourced out from the Campus' Income. An annual budget allocation from of the University's income will be allotted for the facility's operation, subject for approval of the BOR. For Research and Extension Projects that involves the use of the facility, it will be sourced from University RDE Budget which are proposal-based. *The staff for the facility will be hired charged to Campus' Income. In the full operation of the Tissue Culture Laboratory Facility, a laboratory technician will be requested for hiring to be charged in the Agency's Regular Fund.
b. Personnel Sustainability Plan	* Two (2) permanent faculty members will be sent to tissue culture operations training at PhilFIDA Regional Office V. These two faculty members will man the day-to-day operation of the Tissue Culture Laboratory and will perform plant tissue culture processes. * One (1) permanent faculty member will be in-charge of managing plant hardening and greenhouse operations to ensure healthy plant stock is distributed or sold to beneficiaries or clients. He will also take charge of/coordinate the preventive maintenance, calibration, and maintenance of the equipment.

*These three (3) faculty members who will be directly involved in the operations of Tissue Culture Laboratory Facility will be given corresponding deloading on their faculty workload.

* A staff will be in-Charge in the keeping records, documents, maintaining cleanliness in the laboratory and materials used in tissue culture, monitor supplies, proper labelling of culture bottles, keep track of the activities and transactions on the laboratory, and related tasks.

* They will be attending trainings, seminars, workshops and conferences to stay updated with recent developments in tissue culture operations and its management.

Name of Personnel	Position/Designation/Contact Information	Status of Employment
1. Jenny P. Lorio	Associate Professor III/Dean Email: jenny.lorio@parsu.edu.ph Contact No.: 09813863814	Permanent
2. Maria Melania T. Sangalang	Instructor III/Extension Coordinator email: mhel.sangalang@parsu.edu.ph Contact No.: 09084390032	Permanent
3. Thinez B. Bobis	Instructor II/Business Affairs Coordinator email: thinez.bobis@parsu.edu.ph Contact No.: 09338106504	Permanent
4. Laboratory Aide/Staff or Laboratory Technician	BS Biology graduate	Contract of Service

c. Maintenance Sustainability Plan

*The Tissue Culture Laboratory Facility will be part of the Preventive Maintenance of the PPF unit of the University. The over-all management and maintenance of the facility will be spearhead by the project management/personnel.

* The continuous implementation of the project on abaca seedling production and distribution and research on abaca revitalization program will support the operation of the facility.

* Allocation of budget for repairs and maintenance services of the Tissue Culture Facility will be one of the expense items in the Campus budget preparation.

*Periodic repair and maintenance shall have to incorporate on the crafted operation manual. This is a concerned priority in crafting the manual of operation.

*The use of lightings and air-conditioning units shall be of great observance. It should be watched the use of lightings and air-con during operation. One operator should be assigned.

	*The cost of electricity should be watched and monitored. Records of payment of electrical bills should be kept.
d. Promotional Plan	* Information and updates on the presence and operation of the Tissue Culture Laboratory Facility will be posted at the PSU-College of Agribusiness and Community Development (Salogon Campus) official facebook page, in the Android Kiosk that will be installed in the Campus (on going procurement process). * The Campus will promote the facility and services it offers trough a brochure (See Appendix D. Sample Brochure for the Tissue Culture Laboratory Facility).
e. Operational Plan	*An operational plan was crafted for the tissue culture laboratory facility of Partido State University (See Appendix C.). The plan will be presented for inputs of stakeholders including the Department of Agriculture through the MAOs, farmers, faculty researchers, students, and other stakeholders. Thereafter, the operational plan will be submitted for approval of the Administrative Council then the Board of Regents. * A Laboratory Manual will be developed by the faculty in-charge to ensure smooth and proper use of the facility. *There will be corresponding payment for the services of the facility. This payment should be affordable by the clients of the facility. It should be at least 10% higher than the cost of production of the seedlings for sale. The proceeds of sale shall be used for operational expenses of the facility. *5% from the Campus income to augment funds for payment of the operational cost of the facility shall be allotted. The allocation of the fund should pass the approval of the University Board of Regents.
f. Partnerships	*PSU will maintain active partnership with PhilFIDA in its abaca RDE projects. *Linkage with LGU initially with Goa, Tigaon and Sagnay will be forged. *PSU will forged partnership with farmers associations specifically abaca and bamboo farmers association.
g. Research Plan	* The PSU-Salogon Campus will conceptualize RDE programs/projects for its Tissue Culture Facility including: Research: *Development, Survival and Growth Performance of Tissue-Cultured Varieties of Abaca in Partido, Camarines Sur – to be submitted for internal funding *Development, Survival and Growth Performance of Tissue-Cultured Local Varieties of Bamboo in Partido, Camarines Sur – to be submitted for internal funding Extension (Existing): Abaca Seedling Production and Distribution to Farmers in Partido, Camarines Sur

	*An abaca revitalization research project will be crafted for possible external funding.
h. Certifications	*Indicate plans on acquiring certifications/accreditation for the use and operation of the facility (e.g., LTO, CaTO, GMP, FDA, TCL- Accreditation etc.).*
i. Others:	*Include other necessary plans for the sustainability of the upgraded facility.* *A laboratory technician will be requested for hiring when the facility is fully operational. *The unused building at the side of the Tissue Culture Laboratory will be renovated to serve as office of the faculty in-charge and laboratory aide. This is where files, documents, and office works will be done; and the office for receiving clients/stakeholders.

2. Plan of Activities for the remaining project duration

- *Indicate other future activities to be conducted for the remaining project duration*
- *If the project implementation is behind the approved workplan schedule, include a catchup plan in this section.*

Future activities to be conducted for the remaining project duration:

- Following-up the remaining amount to complete payment to the service provider for the construction of the facility.
- Fast-tracking of the procurement of equipment and supplies amounting to P880,000.00 for 2024.
- Crafting of the Tissue Culture Laboratory Operational Plan.

Catch-up plan:

- The operational plan will consider inputs from the stakeholders including farmers, researchers, extensionists, students, the Department of Agriculture through its Municipal Agriculture Offices in nearby localities, Sangguniang Bayan, and others. Then, it will be presented to the Administrative Council and BOR for approval.
- Allocation of annual budget for the operations and maintenance of the facility, for BOR approval.
- Revision and finalization of IEC material such as brochure for the promotion of the Tissue Culture Laboratory Facility.

III. ATTACHMENTS

1. Liquidation Documents
2. Memorandum Receipts/ Property Acknowledgment Receipts of All Equipment Purchased
3. Picture of Project Signage
4. Notice to Proceed
5. List of Personnel Involved and their Roles/Responsibilities
6. List of Specific Beneficiaries
7. Photos and description of the old and newly upgraded/established facility
8. Photos and description of the old and newly purchased equipment
9. Workplan Schedule
10. Pictures and Description of Activities Conducted
11. Justifications for any Discrepancies Vis-À-Vis Approved Proposal (Specifications, Quantity, Quality, Etc.)
12. Working Drawings

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

GUIDELINES FOR THE PREPARATION OF TERMINAL REPORT ATTACHMENTS FOR RESEARCH FACILITIES DEVELOPMENT

1. **Liquidation Documents**
   PLEASE DO NOT BIND THIS when submitting the original hardcopy.
   a. Audited Financial Report
      (3 Original hardcopy; This must be signed by the accountant and verified by a COA representative or stamped "received" by COA)
   b. Report of Checks Issued/ Report of Disbursement
      (3 Original hardcopy; This must be signed by the accountant and verified by a COA representative or stamped "received" by COA)
   c. Journal Entry Vouchers
      (3 Copies; These may be original copies or photocopies stamped "certified true copy" by the agency's accountant)

2. **Memorandum Receipts/ Property Acknowledgment Receipts of All Equipment Purchased**
   Provide clear scanned copies of all the MRs/PARs of the procured equipment

3. **Picture of Project Signage**
   Provide clear pictures of the project signage

4. Notice to Proceed



PARTIDO STATE UNIVERSITY

ParSU OP Office of the President <op@parsu.edu.ph>

Notice to Proceed ACEF-RFDG Project (Partido State University)

Institutional Development Section <ids@bar.gov.ph> Fri, Jul 7, 2023 at 9:35 AM
To: Joel Sadol <joel.sadol@parsu.edu.ph>, jenny.lorie@parsu.edu.ph, salogon.campus@parsu.edu.ph, op@parsu.edu.ph
Cc: Institutional Development Section <ids@bar.gov.ph>

Dear Proponents,

This is to officially inform you of the approval of the project titled ***"Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus"*** with funding support of **Php 1,589,474.50.** This serves as an official **NOTICE TO PROCEED** to the implementation of project activities from **June 5, 2023 to June 4, 2024.**

Kindly schedule the conduct of an inception meeting which shall serve as a venue to level off on the project implementation and other requirements/deliverables of the project. Also, please see attached signed Notice to Proceed, MOA and Approved Proposal, for your reference.

Please acknowledge receipt of this email.

Thank you.

--

Kind regards,

INSTITUTIONAL DEVELOPMENT SECTION
Research Program Development Division
Bureau of Agricultural Research
(02) 8461-2800 / -2500
www.bar.gov.ph
3F RDMIC Bldg. Elliptical Rd. cor. Visayas Ave., Diliman, QC

Create your own email signature

3 attachments

NTP - 5 - ParSU (Upg... Tissue Culture Lab...) sgd.PDF
188K

MOA - 5 - ParSU (Upg... Tissue Culture Lab...) sgd.PDF
1272K

DPP - 5 - ParSU (Upg... Tissue Culture Lab...) sgd.PDF
2678K

PARTIDO STATE UNIVERSITY
OFFICE OF THE PRESIDENT
RECEIVED
BY: _____ DATE: 7/10/23

Republic of the Philippines
OFFICE OF THE SECRETARY
Elliptical Road, Diliman
1100 Quezon City

May 31, 2023

DR. RAUL G. BRADECINA
President
Partido State University
Goa, Camarines Sur

ATTENTION : **ENGR. JOEL P. SADOL**
Project Leader

Subject : **Notice to Proceed and Fund Release**

Dear **President Bradecina**:

This is to officially inform you of the approval of the project titled **"Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus"** with funding support of **Php 1,599,474.50**. This serves as an official **NOTICE TO PROCEED** to the implementation of project activities from **June 5, 2023 to June 4, 2024**. The full release of the CY 2023 fund for the operation and implementation of the abovementioned project was transferred to the official depository bank of the **PARTIDO STATE UNIVERSITY** with the following details:

Account Name	Account Number	Amount (PhP)	LDDAP-ADA No.	Date of Fund Transfer
Partido State University	2082-1016-78	1,599,474.50	183-04-007-2023	April 26, 2023

For the acknowledgment of funds received for the project, may we request your office to submit the official receipt to DA Cashier's Office within one (1) week after the receipt of this document for the amount credited to your bank account, with an acknowledgment letter signed by the head of the implementing agency.

Kindly schedule the conduct of an inception meeting which shall serve as a venue to level off on the project implementation and other requirements/deliverables of the project. The meeting should be participated by the project stakeholders (e.g. project team, BAR, ACEF PMO, DA RFO, etc.).

In addition, may we remind the project leaders that there should be signage/s within ten (10) days after the issuance of the Notice of Award of the project placed in conspicuous areas preferably in front of the agency/institution's building and at the project site/s in order to properly acknowledge and give due recognition to the R&D assistance and funding support provided by the Department of Agriculture.

Masaganang Agrikultura, Maunlad na Ekonomiya

1. DA and Implementing Agency Logo
2. Project Title
3. Funding/Coordinating Agency
4. Implementing/Collaborating Agency
5. Project Location

Thank you and best regards.

Very truly yours,

DOMINGO F. PANGANIBAN
Senior Undersecretary

5. List of Personnel Involved and their Roles/Responsibilities

Project Title: Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus

Name of Personnel	Position	Contact Details	Sex (M/F)	Senior Citizen (Y/N)	Persons with Disability (Y/N)	Indigenous People (Y/N)
1. Jenny P. Lorio	Associate Professor III	*email: jenny.lorio@parsu.edu.ph Mobile No.:09813863814*	*F*	*N*	*N*	*N*
2. Maria Melania T. Sangalang	*Instructor III*	*email: mhel.sangalang@parsu.edu.ph Mobile No.: 09084390032*	*F*	*N*	*N*	*N*
3. Thinez B. Bobis	*Instructor II*	*email: thinez.bobis@parsu.edu.ph Mobile No.: 09338106504*	*M*	*N*	*N*	*N*
4. Laboratory Aide/Staff	*BS Biology graduate*	**for hiring*				
5.						

6. List of Specific Beneficiaries

Indicate the target groups or individuals who will benefit from the project. Please also fill up the inventory of beneficiaries' template.

Project Title: Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus

Next Users *Name the people from your institution who will be the enabler of the facility's services*						
Specific Beneficiary	**Number of Beneficiaries**	**Location**	**Sex (M/F)**	**Senior Citizen (Y/N)**	**Persons with Disability (Y/N)**	**Indigenous People (Y/N)**
1. Students	*200*	*ParSU-Salogon Campus*	*M, F*	*N*		
2. Faculty	*10*	*ParSU-Salogon Campus*	*M, F*	*N*		
3. Researchers	*20*	*ParSU-Salogon Campus*	*M, F*	*N*		
4. Extensionists	*20*	*ParSU-Salogon Campus*	*M, F*	*N*		
5.						

End Users *Technology Adopters or Actual users/beneficiaries of the facility's services* *(Farmer/ Fisherfolks/ Associations/Cooperatives/ MSMES/ Students/ Faculty/ Researchers, Etc.)*						
Specific Beneficiary	**Number of Beneficiaries**	**Location**	**Sex (M/F)**	**Senior Citizen (Y/N)**	**Persons with Disability (Y/N)**	**Indigenous People (Y/N)**
1. Abaca Farmers *- Salog Abaca Association* *-Tadyong Tribal Farmers Association* *-Agta Tribe Organization*	*100*	*4th District, Camarines Sur*	*M, F*			

-Bicol Cacao growers Association, Inc.						
2. Bamboo Farmers	*100*	*4th District, Camarines Sur*	*M, F*			
3.						
4.						
5.						

7. Photos and description of the old and newly upgraded/established facility

Project Title: <u>Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus</u>




Side view of the existing but non-functional building at PSU-Salogon



Front view of the existing but non-functional building at PSU-Salogon



Front & Side views of the established Tissue Culture Laboratory Facility

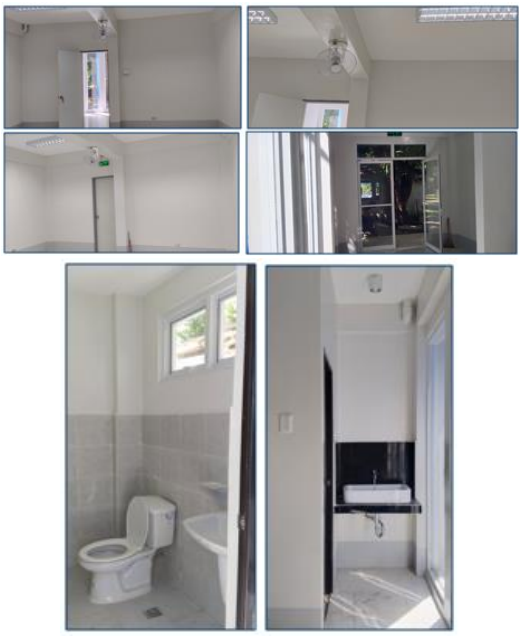

Inside of the established Tissue Culture Laboratory Facility

8. Photos and description of the old and newly purchased equipment

Project Title: <u>Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus</u>

Old Equipment	New Equipment	Specifications	Cost, Php	Quantity	Remarks /Status (For Procurement, Procured, Delivered, Installed, Tested, Operational)
	Laminar flowhood/Laminar Flow Cabinet, vertical type	Flow Type: Vertical Voltage/Frequency(V/Hz): AC220/50 Power(W): 1200 Vibration Amplitude(UM): 2 Exhaust Filter Typical Efficiency: H13 HEPA,99.99%@0.3um Average Velocity (m/s): 0.2-0.5 Fluorescent Lamp Intensity(Lux):>_300 Net/Gross Weight (approx.): 330-392lbs. Sound Emission dB(A): 62 Internal Dimensions(W*D*H): 1300*516*520mm External Dimensions(W*D*H): 1370*611*1754mm Cleanliness Classification: ISO 14644.1 Class 5	150,000.00	1	For procurement
	Autoclave machine/ Sterilizer	Volume: 39L capacity Rated pressure: 0.14~0.16MPa	100,000.00	2	For procurement

		Rated Working Temperature: 126°C Max. Safety Pressure: 0.165MPa Electricity: AC 220V/ 50Hz, 2.5kW Electricity: AC 220V/ 50Hz, 2.5kW			
	Laboratory Rack	Material: Mild Steel Size of Rack: 48x21 inch Distance Between Each Rack: 15inches Surface Finish: Powder Coated No. of Layers: 2x5 layers	100,000.00	1	For procurement
	Food Grade Stainless Steel Table	Dimension: Length 2.0 meters x Width 0.5 meters x Height 0.75 meters	200,000.00	2	For procurement
	Digital Weighing Scale	Weighing Capacity: 60kg. Scale type: Platform Interface type: RS232 Resolution: 10g,20g	100,000.00	1	For procurement
	Chemicals			(in bottles)	
	Ammonium Nitrate, Purified 500g		14,300.00	1	For procurement
	Potassium Nitrate, 500g		14,300.00	1	For procurement
	Calcium Chloride Dihydrate, 500g		1,000.00	1	For procurement

	Magnesium Sulfate Anhydrous, 500g		1,350.00	1	For procurement
	Potassium Dihydrogen Phosphate, 500g		1,500.00	1	For procurement
	Manganous Sulfate, Monohydrate,99% AR/ACS 500g		3,500.00	1	For procurement
	Boric Acid, Granular 500g		1,500.00	1	For procurement
	Zinc Sulfate, heptahydrate 500g, power Hi-media		1,250.00	1	For procurement
	Potassium Iodide 500g		5,000.00	1	For procurement
	Sodium Molybdate, Dihydrate reagent,crstal ACS 500g		9,000.00	1	For procurement
	Copper(II) Sulfate, Anhydrous 500g		2,000.00	1	For procurement
	Cobalt(II) Chloride, hexahydrate, 500g		8,000.00	1	For procurement
	Iron(II)Sulfate Heptahydrate 500g		750.00	1	For procurement
	EDTA, Disodium Salt 500g		2,000.00	1	For procurement
	Myo Inositol		3,500.00	1	For procurement
	PTC Agar 500g		17,500.00	5	For procurement
	Activated Charcoal powder, Hi-PR 500g		1,000.00	1	For procurement

	Nicotinic Acid, 99.5% Extra pure, 100g		1,500.00	1	For procurement
	Pyridoxine HCl(Vit. B6), 100g		1,750.00	1	For procurement
	Thiamin HCl(Vit. B1), 100g		2,000.00	1	For procurement
	Folic Acid		1,700.00	1	For procurement
	d-Biotin, Hi-media 100g		4,000.00	1	For procurement
	Glycine Hi-media 100g		4,000.00	1	For procurement
	6-Benxyladenine (6-BAP) HI-media 5g		6,500.00	1	For procurement
	Indole-3-Butyric Acid (IBA) HI-media 5g		5,000.00	1	For procurement
	Potassium Hydroxide pellets, 500g		1,200.00	1	For procurement
	Hydrochloric Acid		3,200.00	1	For procurement
	95% Ethyl Alcohol, TG, gallon		4,000.00	1 gal	For procurement
	Sodium Chloride, 500g Hi-media		1,000.00	1	For procurement
	Potassium Hydrogen Orthophosphate, 500g		1,000.00	1	For procurement
	Di-sodium Hydrogen Orthophosphate Anhydrous, 500g		1,500.00	1	For procurement
	Pottasium Chloride, AR 500g		1,500.00	1	For procurement

	Sodium Carbonate Anhydrous, AR, 500g		1,000.00	1	For procurement
	Sodium Hydrogen Carbonate, Extra Pure AR, 99.5% 500g		1,000.00	1	For procurement
	Diethanolamine		8,500.00	1	For procurement
	Sodium Azide, Reagent plus, >99.5%		3,500.00	1	For procurement
	Hydrochloric Acid,1N 500ml		3,200.00	1	For procurement
	Sodium Hydroxide Pellets 500g NaOH=40.00		1,500.00	1	For procurement
	Tween 20 Surfact-Amps; Detergent Solution 1L		2,500.00	1	For procurement
	pNPP tablets 5mg		3,500.00	40 pcs	For procurement
	GARAP		38,000.00	1	For procurement
	96-well ELISA microplates, 12*c8, high binding white		10,000.00	100 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 20ml		1,750.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 30ml		2,250.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 50ml		2,750.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 100ml		3,500.00	5 pcs	For procurement

	Glass Measuring Cup, Heat resisting, 200ml		4,250.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 250ml		4,750.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 500ml		5,250.00	5 pcs	For procurement
	Glass Measuring Cup, Heat resisting, 1000ml		5,500.00	5 pcs	For procurement
	Total		**880,000,000.00**		

Source: PhilFIDA Region V; List of equipment, materials and supplies for Diagnostic Laboratory, Preparation Room, Ante-Room, Inoculation and Culture Room

9. WORKPLAN SCHEDULE

Project Title: **Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus**

Starting Date: *23-06-05* | **Completion Date:** *24-09-04* | **Duration:** *15 months*

Objectives	Activities	Expected Results/ Outputs	Responsible Person(s)	Resources Required	Schedule of Activities (Months)															Budget Required
					1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	
1. To renovate unoccupied building of Partido State University at Salogon Campus adoptable to Tissue Culture Facility.	Procurement Process Upgrading of Tissue Culture Facility at PSU-Salogon Campus.	Completion of the upgrading of Tissue Culture Facility at PSU-Salogon Campus.	Project Leader Implementing Agency: Partido State University (PPF, Procurement and Budget Sections)	Manpower Construction materials Budget																P 1,599,474.50 (Source: DA-BAR-ACEF) Contractor/Supplier: Seven R Construction Partial billing: P820,365.37 Date: April 24, 2024 Payment after completion: P799,109.13
2. To procure new apparatuses and equipment in replaceme	Preparation of procurement documents (PPMP, PR, PO) for the apparatuses and	Provision of the necessary apparatuses and equipment to start the operation	Project Leader Implementing Agency: Partido State University (PPF, Procurement	Tissue Culture Apparatus and equipment Budget																P 880,000.00 (Source: Partido State University-proposal) P4,898,262 (Detailed computation of laboratory equipment, supplies and materials)

nt of outdated and non-functional apparatuses and equipment of existing tissue culture facility.	equipment for the Tissue Culture Facility. Coordination with the In-charge of Tissue Culture Laboratory at PhilFIDA Legazpi City will be done for the accurate identification and specifications of apparatuses and equipment.	of the facility.	and Budget Sections)																
3. To establish operational plan for Tissue Culture Facility	Crafting of operational plan for the facility, anchored to academic and RDE	Draft operational Plan for the Facility for approval by the	Project Leader Facility In-charge Faculty Researchers	Manpower Budget															

	agenda of the University and Salogon Campus.	University President and BOR, specifying its use for instruction, research and extension services to faculty and student researchers in the Bicol Region.	and Extension Implementers																

Prepared by:

Jenny P. Lorio, PhD.
Co-Project Leader

10. Pictures and Description of Activities Conducted

May include Inauguration, Production, Installation, Inspection, Testing of Equipment, Trainings, Seminars, Meetings

- Monitoring visit by DA-BAR ACEF Team on April 16, 2024







11. Justifications for any Discrepancies Vis-À-Vis Approved Proposal (Specifications, Quantity, Quality, Etc.)

- Change in facility design

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur, Philippines

24 July 2023

Hon. DOMINGO F. PANGANIBAN
Senior Undersecretary, Department of Agriculture
Chairman, ACEF Executive Committee
Elliptical Road, Diliman, Quezon City
Philippines

THRU: **JUNEL B. SORIANO, PhD.**
Director
DA- Bureau of Agricultural Research

Dear **Sir,**

This is to request your permission to allow us to revise the plan of the tissue culture laboratory facility that your agency have budgeted on our behalf. The revision we made was focused primarily on the aesthetic consideration of the frontage of the facility. This will not change the functionality of the facility and it will not have additional budget for its revision. It has the same floor area but only the area for stairs going to slab roofing and additional structure to beautify the facility frontage will be provided and added in the plan.

Attached is the perspective views of the approved and revised design of tissue culture laboratory facility for your perusal.

We are hoping for your approval of this regard.

Sincerely,

RAUL G. BRADECINA, PhD.
SUC President III

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur, Philippines



Approved Designed of the Proposed Tissue Culture Laboratory Facility



Revised Designed of the Proposed Tissue Culture Laboratory Facility

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Salogon Campus
Salogon, San Jose, Camarines Sur, Philippines

18 August 2023

DR. RAUL G. BRADECINA
SUC President III
This University

Dear Sir,

The DA-BAR, funding agency of our project entitled "Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus" requires the signatory for any request revision of plans of the project shall be the head of the agency. The PPF personnel of our university and I decided that the frontage of the building of such project should be revised in order its aesthetic consideration met.

In this connection, I would like to request that you affix your signature on the letter I wrote requesting DA-BAR to allow us to go with the revision of the plan. The revision does not entaill additional funding to DA-BAR and to our university.

I am hoping your kind consideration.

Sincerely,

JOEL P. SADOL
Project Leader/Campus Dean

PARTIDO STATE UNIVERSITY
OFFICE OF THE PRESIDENT
RECEIVED
BY: _____ DATE AUG 18 2023
9:230



REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

Reference No. 2023-09-21
September 7, 2023

RAUL G. BRADECINA, Ph.D.
SUC President III
Partido State University
Goa, Camarines Sur

Attention: **ENGR. JOEL P. SADOL**
Project Leader

Subject: **Approval of Request for Change in Facility Design**

Dear **President Bradecina:**

This refers to the project titled **"Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus"** under the Agricultural Competitiveness Enhancement Fund (ACEF).

Please be informed that your request to revise the frontage design of the tissue culture laboratory has been **approved**. We took note of the latest development and the improvements made which do not require additional budget or any changes in the program of works.

We look forward to the completion of the project activities within the approved project duration and the submission of all the project deliverables.

Thank you very much.


Very truly yours,

JUNEL B. SORIANO, Ph.D.
Director

Cc: Department of Agriculture – ACEF Program Management Office

www.bar.gov.ph DABAROfficial

- Extension for project extension

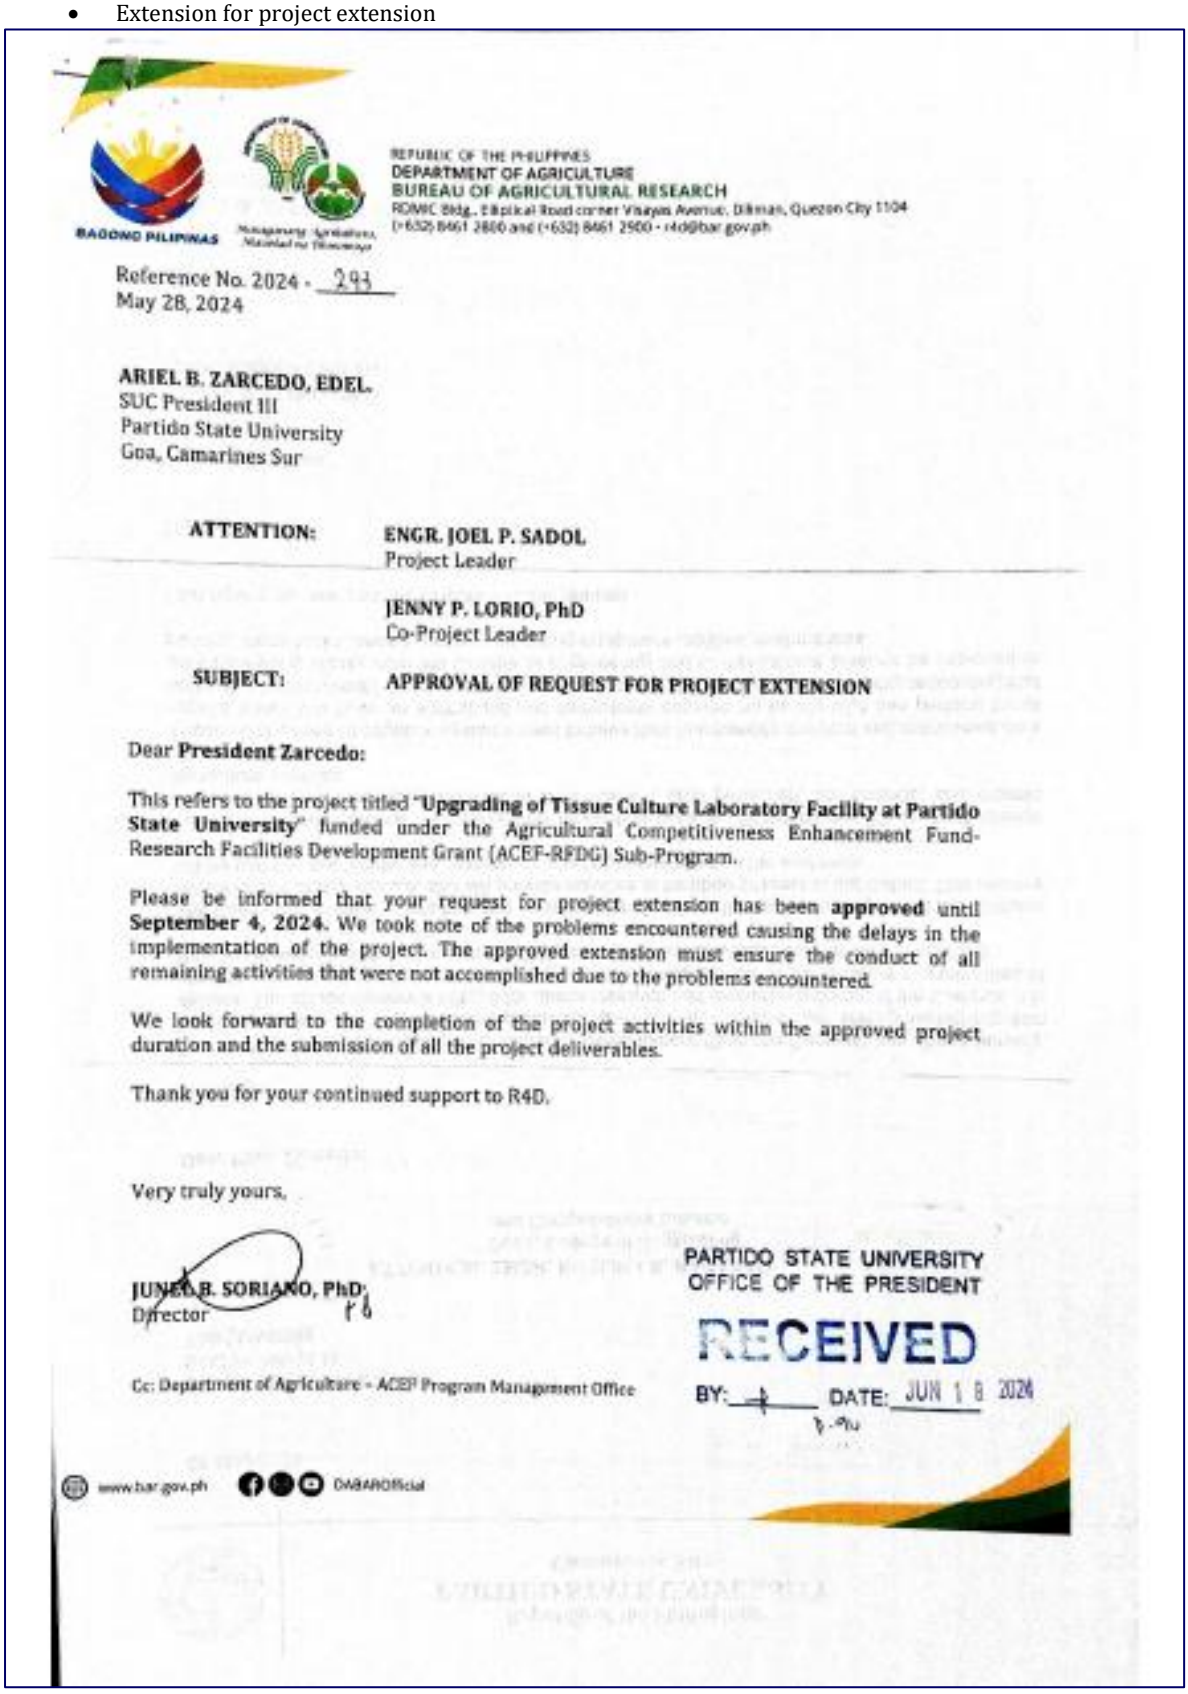

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 - r4d@bar.gov.ph

Reference No. 2024 - 293
May 28, 2024

ARIEL B. ZARCEDO, EDEL.
SUC President III
Partido State University
Goa, Camarines Sur

ATTENTION: **ENGR. JOEL P. SADOL**
Project Leader

JENNY P. LORIO, PhD
Co-Project Leader

SUBJECT: **APPROVAL OF REQUEST FOR PROJECT EXTENSION**

Dear **President Zarcedo:**

This refers to the project titled "**Upgrading of Tissue Culture Laboratory Facility at Partido State University**" funded under the Agricultural Competitiveness Enhancement Fund-Research Facilities Development Grant (ACEF-RFDG) Sub-Program.

Please be informed that your request for project extension has been **approved** until **September 4, 2024.** We took note of the problems encountered causing the delays in the implementation of the project. The approved extension must ensure the conduct of all remaining activities that were not accomplished due to the problems encountered.

We look forward to the completion of the project activities within the approved project duration and the submission of all the project deliverables.

Thank you for your continued support to R4D.

Very truly yours,

JUNEL B. SORIANO, PhD
Director

PARTIDO STATE UNIVERSITY
OFFICE OF THE PRESIDENT
RECEIVED
BY: DATE: JUN 18 2024

Cc: Department of Agriculture - ACEF Program Management Office

www.bar.gov.ph DABAROfficial

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur

May 22, 2024

FRANCISCO P. TIU LAUREL JR.
Secretary, Department of Agriculture and
Chair, ACEF Executive Committee

THRU: **JUNEL B. SORIANO**
Director
DA-Bureau of Agricultural Research

Dear Sir,

This is to humbly request for an extension period for the implementation of the project entitled "Upgrading of Tissue Culture Laboratory Facility of Partido State University in Salogon Campus". The project duration is 12 months from June 5, 2023 to June 4, 2024. This request is due to the following reasons:

- The process of sourcing for a supplier to conformance with the Notice of Award and Contract Agreement took so long (more than six months) from the date the Notice to Proceed and Fund from DA-BAR ACEF was released to the Partido State University.
- It was only in February 26, 2024 that the Contractor/Supplier started the upgrading/construction of the Tissue Culture Facility.
- As of this date, May 22, 2024, the project is on-going specifically working on the painting of the facility, provision of doors and windows, lightings, and other finishing works.

In this light, an extension period from June 5, 2024 to December 4, 2024 is requested to finish the project and disburse the necessary amount to the contractor/supplier.

I am hoping for your affirmative response on this matter.

Thank you very much.

Respectfully yours,


In behalf of the Project Leader:

JENNY P. LORIO
Co-Project Leader

Endorsed:

ARNEL B. ZARCEDO, EDEL.
SUC President III
Partido State University

Received by:
05-22-24

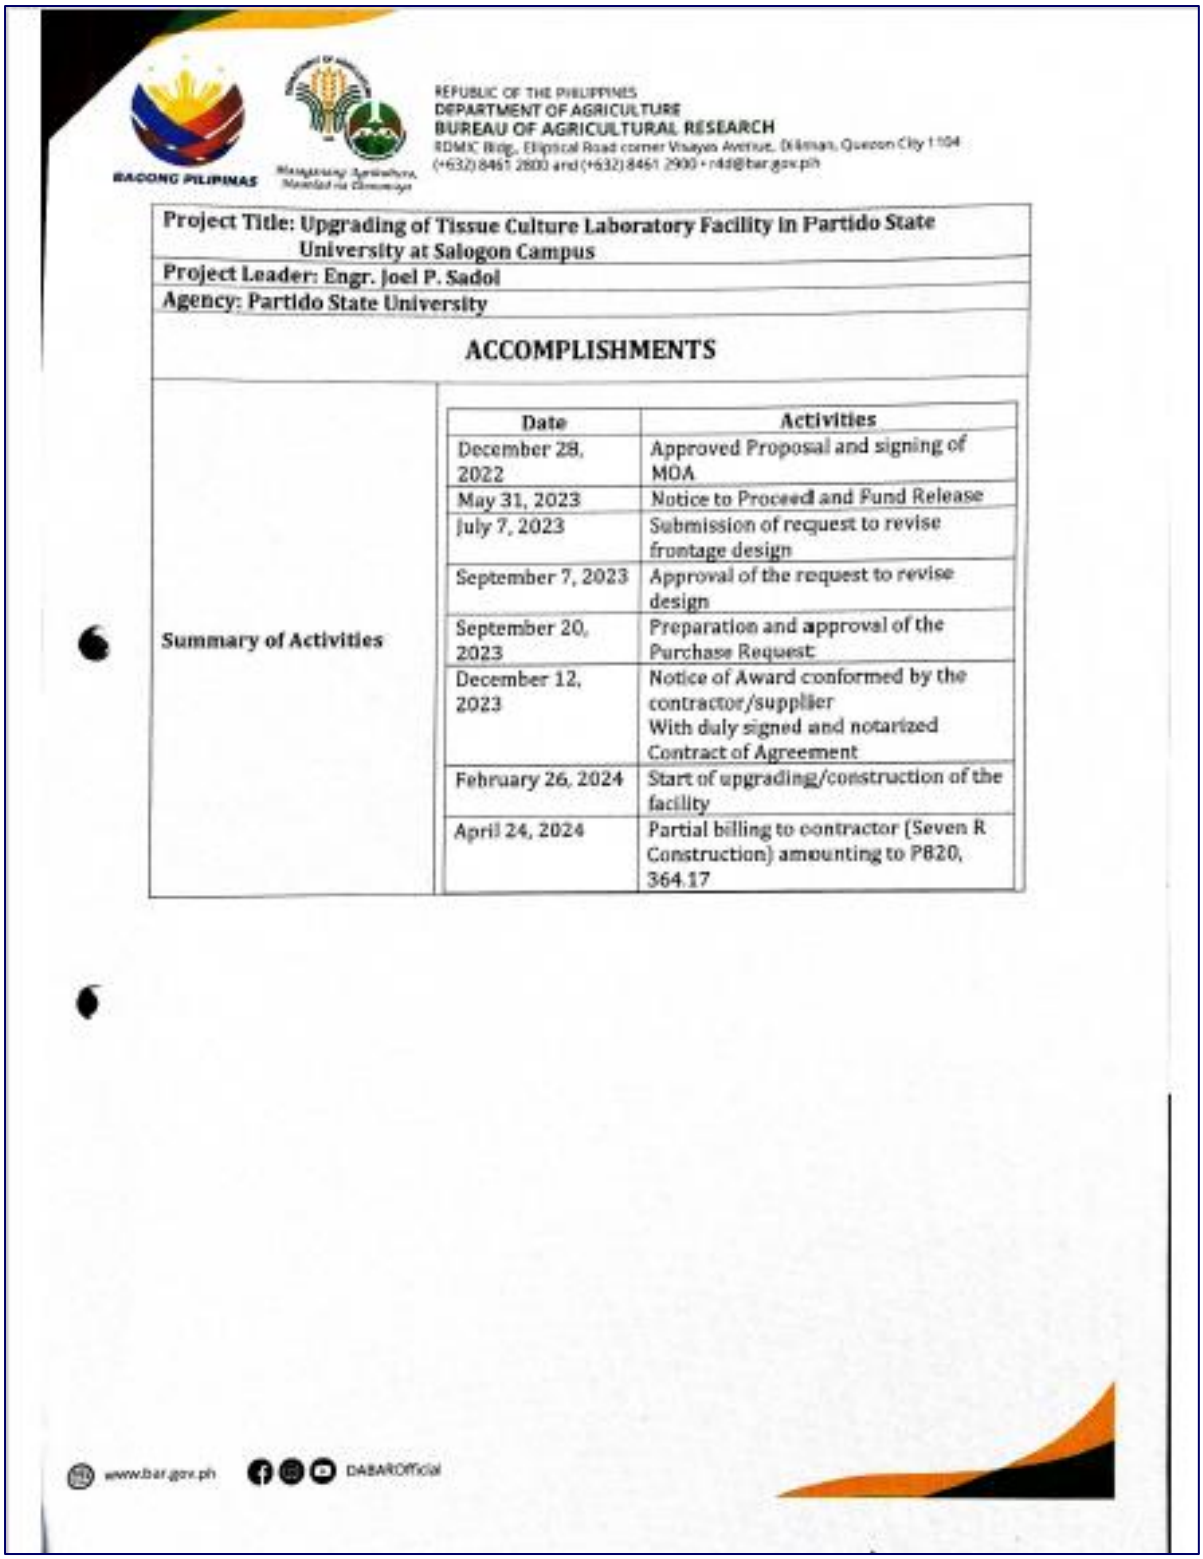

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

Project Title: Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus	
Project Leader: Engr. Joel P. Sadol	
Agency: Partido State University	
ACCOMPLISHMENTS	
Summary of Activities	

Date	Activities
December 28, 2022	Approved Proposal and signing of MOA
May 31, 2023	Notice to Proceed and Fund Release
July 7, 2023	Submission of request to revise frontage design
September 7, 2023	Approval of the request to revise design
September 20, 2023	Preparation and approval of the Purchase Request
December 12, 2023	Notice of Award conformed by the contractor/supplier With duly signed and notarized Contract of Agreement
February 26, 2024	Start of upgrading/construction of the facility
April 24, 2024	Partial billing to contractor (Seven R Construction) amounting to PB20, 364.17

www.bar.gov.ph DABAROfficial

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur

WORKPLAN SCHEDULE

Project Title: **Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salogon Campus**

Starting Date: *(24-06-05)*			**Completion Date:** *(24-12-04)*		**Duration:** *(6 months)*											
Objectives	**Activities**	**Expected Results/ Outputs**	**Responsible Person(s)**	**Resources Required**	**Schedule of Activities**											**Budget Required**
					Months											
					1	2	3	4	5	6	7	8	9	10	11	12	
1. To renovate unoccupied building of Partido State University at Salogon Campus adoptable to Tissue Culture Facility.	Remaining activities/finishing works on the Tissue Culture Facility at PSU-Salogon Campus.	Completion of the upgrading of Tissue Culture Facility at PSU-Salogon Campus.	Project Leader Implementing Agency: Partido State University (PPF, Procurement and Budget Sections)	Manpower Construction materials Budget													P 1,599,474.50 (Source: DA-BAR ACEF) Contractor/Supplier: Seven R Construction Partial billing: P820,364.17 Date: April 24, 2024 Payment after completion: P799,110.33

Respectfully yours,

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur

2. To procure new apparatuses and equipment in replacement of outdated and non-functional apparatuses and equipment of existing tissue culture facility.	Preparation of procurement documents (PPMP, PR, PO) for the apparatuses and equipment for the Tissue Culture Facility. Coordination with the In-charge of Tissue Culture Laboratory at PhilFIDA Legazpi City will be done for the accurate identification and specifications of apparatuses and equipment.	Provision of the necessary apparatuses and equipment to start the operation of the facility.	Project Leader Implementing Agency: Partido State University (PPF, Procurement and Budget Sections)	Tissue Culture Apparatus and equipment Budget	

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur

3. To establish operational plan for Tissue Culture Facility	Crafting of operational plan for the facility, anchored to academic and RDE agenda of the University and Salogon Campus.	Draft operational Plan for the Facility for approval by the University President and BOR, specifying its use for instruction, research and extension services to faculty and student researchers in the Bicol Region.	Project Leader Facility In-charge Faculty Researchers and Extension Implementers	Manpower Budget		P 880,000.00 (Source: Partido State University)

Prepared by:

In behalf of the Project Leader:

JENNY B. LORIO, PhD.
Co-Project Leader

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

Appendix 35

REPORT OF CHECKS ISSUED
Period Covered: January-April 2024

Entity Name: Partido State University
Fund Cluster:07
Bank Name/Account No.: LBP/2082-1016-78

Report No.: 01
Sheet No.: 01

Check		DV/Payroll No.	ORS/BURS No.	Responsibility Center Code	Payee	UACS Object Code	Nature of Payment	Net Amount	Tax/GSDP/ATC	Amount
Date	Serial No.									
04/24/2024	834476	40065	06-07308603-2023-12-336	01	Seven "R" Construction & Supply	20401010000	Payment for the partial billing for the project on upgrading of tissue culture laboratory in Partido State University-Salogon Campus	570,222.68	250,142.69	820,365.37
TOTAL										820,365.37

CERTIFICATION

I hereby certify on my official oath that this Report of Checks Issued is One (1) sheet(s) is full, true and correct statement of all checks issued by me during the period stated above for which Check No. 834476 inclusive, were actually issued by me in payment for obligations shown in the attached disbursement vouchers/payroll.

TOMAS C. SALAS JR., DBA
Name and Signature of Disbursing Officer/ Cashier

Administrative Officer V
Official Designation

Date

Reviewed by:
ENGR. JOVINA A. BAUTISTA
06-03-24

Republic of the Philippines
PARTIDO STATE UNIVERSITY
Camarines Sur

RECEIVED
PARTIDO STATE UNIVERSITY
COMMISSION ON AUDIT
Date: 5/31/2024
Signature

AUDITED FINANCIAL REPORT
As of April 30, 2024

Project Title: Upgrading of Tissue Culture Laboratory Facility in Partido State University at Salcgon Campus
LDDAP Number: JEV#23-06-0[illegible]9
Proponent: Engr. Joel P. Sadol/Dr. Jenny P. Lorio
Date Released: April 27, 2023
Implementing Agency: Partido State University
Total Amount: Php 1,599,474.50

Expense Code (Particulars)	Approved Budget (A)	Amount Released (B)	Disbursements (C)	Balance To Date (B-C)
Personnel Services (PS)	-	-	-	-
Subtotal	-	-	-	-
Maintenance and Other Operating Expenses (MOOE)	-	-	-	-
Subtotal	-	-	-	-
Equipment Outlay (EO)				
A. Equipment				
1. Equipment 1				
2. Equipment 2				
3. Equipment n				
B. Upgrading of Facility	1,599,474.50	1,599,474.50	820,365.37	779,109.13
Subtotal	1,599,474.50	1,599,474.50	820,365.37	779,109.13
Administrative Cost	-	-	-	-
Subtotal	-	-	-	-
TOTAL	1,599,474.50	1,599,474.50	820,365.37	779,109.13

PREPARED BY:
JENNY P. LORIO
Co-Project Leader
Date

CERTIFIED CORRECT:
NANCY C. ENCINAS, CPA
Chief Accountant
Date

APPROVED BY:
ARNEL B. ZARCEDO, EDEL
Agency Head
Date

VERIFIED BY:
Verified and completeness and accuracy of recording. Subject to further audit.
LOU ANTONETTE BOSITAÑO
Auditor
May 31, 2024
Date

Received by:
ENGR. CHARMIE A. [illegible]
05-05-24

SUBSIDIARY LEDGER

Entity Name: **Partido State University** Fund Cluster: 07

Account of: **DA-BAR**
Office/Address:
Contact Person: **Jenny P. Lario**
Contact Number/Email Address: **jenny.lario@parsu.edu.ph**

Account Code
GL 2 04 01 010 00
SL 2 04 01 010 00 - Tissue Culture Laboratory

Date	Particulars	Ref	Amount		
			Debit	Credit	Balance
12/31/2023	Fund transfer from DA-BAR for Tissue Culture Laboratory Facility in PSU-Sabogon Campus received on April 27, 2023	JEV#23-06-[illegible]		1,599,474.50	1,599,474.50
01/31/2024	**No Transaction for January 2024**				1,599,474.50
02/29/2024	**No Transaction for February 2024**				1,599,474.50
03/31/2024	**No Transaction for March 2024**				1,599,474.50
04/24/2024	Payment for the 1st partial billing (Seven "R" Construction & Supply)	Ck No. 834476	820,365.37		779,109.13
	Balance as of April 30, 2024				779,109.13

Prepared by:

REY M. BALATICO
Accountant I


Certified Correct:

NANCY C. ENCINAS, CPA
Accountant III

COMMISSION ON AUDIT
PARTIDO STATE UNIVERSITY
RECEIVED
Date: 05/31/2024
Signature:

Received by:
[illegible]
04-25-24


12. Working Drawings

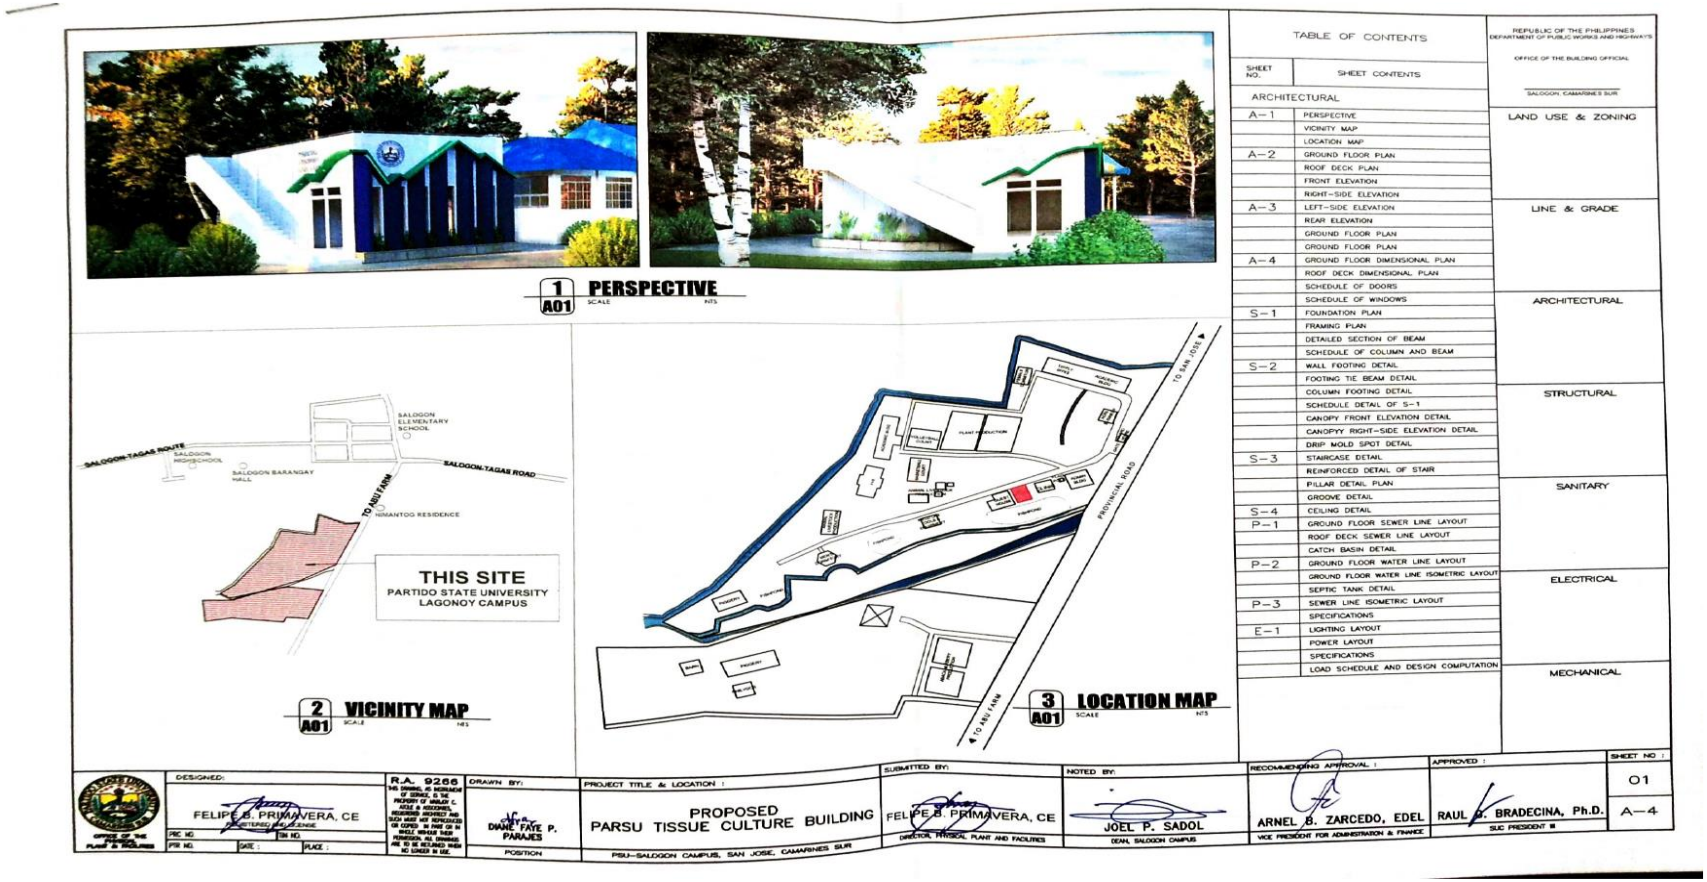

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS


Masaganang Agrikultura, Maunlad na Ekonomiya

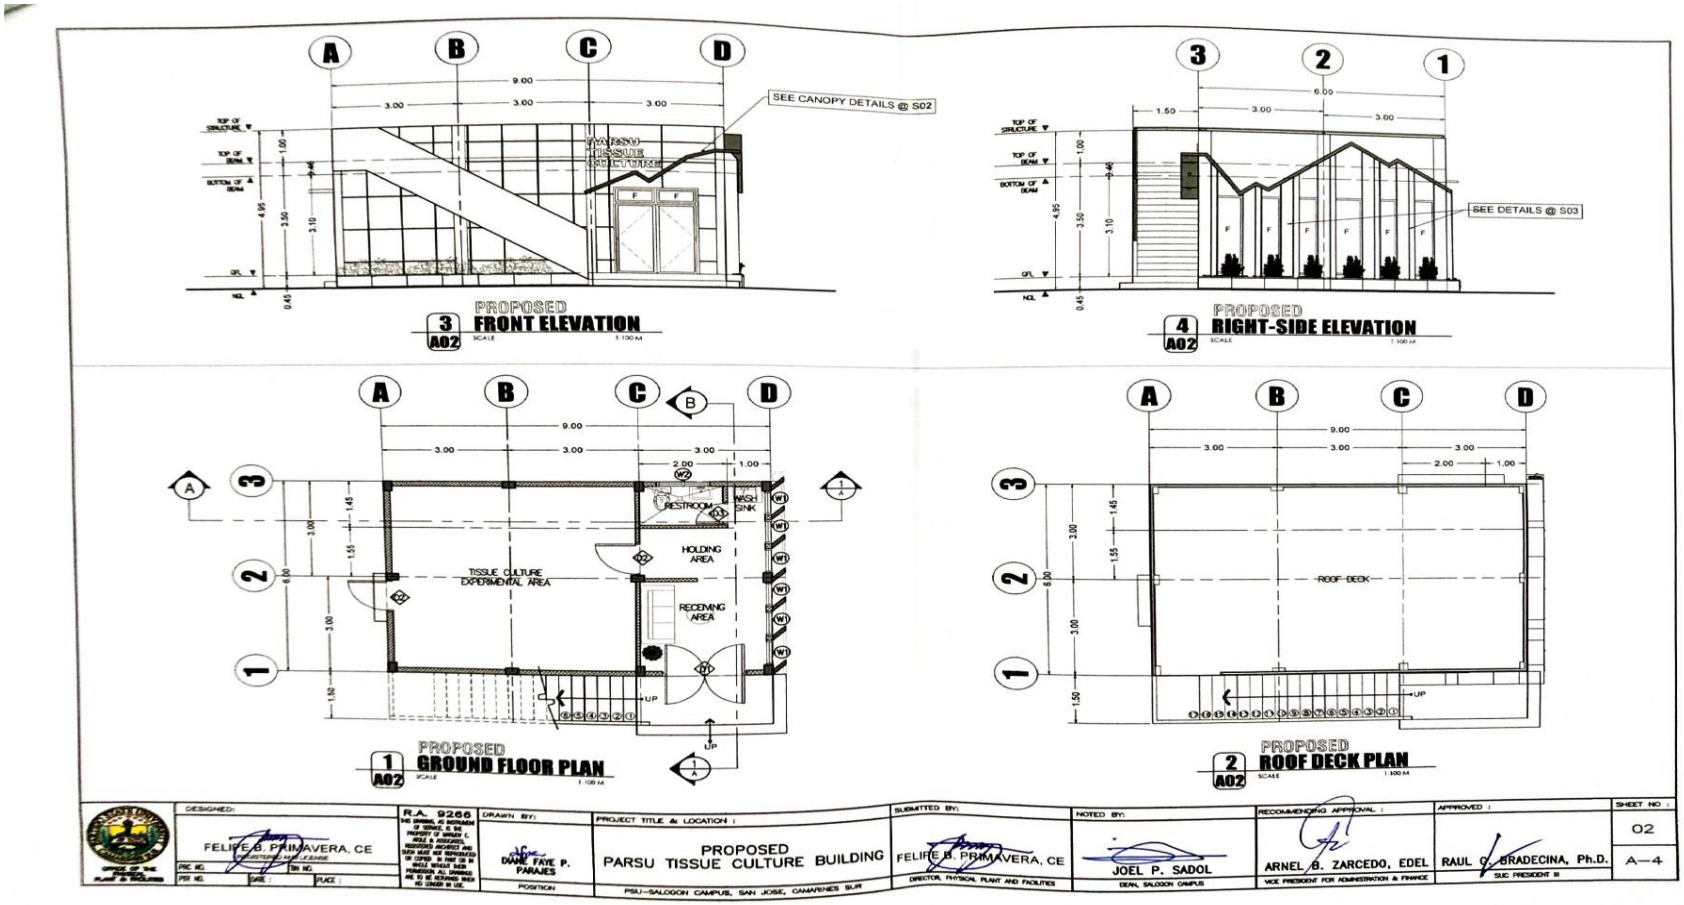

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

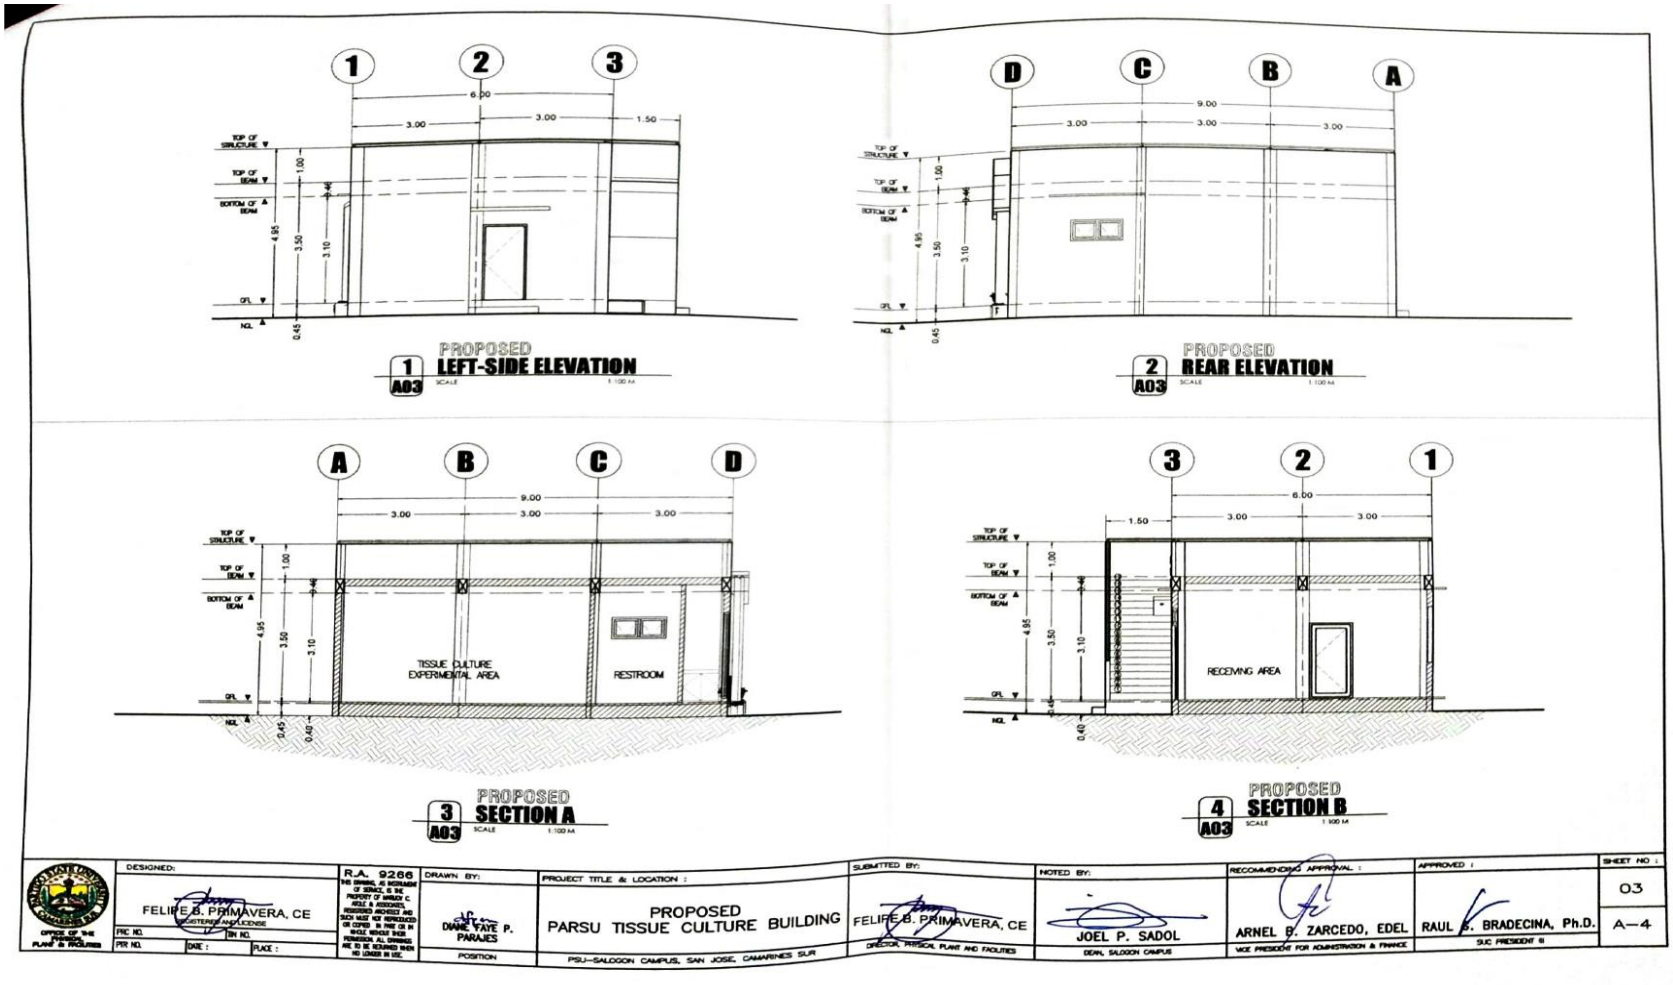


DESIGNED: FELIPE B. PRIMAVERA, CE (REGISTERED ENGINEER AND LICENSE; PRC NO.; TIN NO.; PTR NO.; DATE:; PLACE:)	R.A. 9266 THE ORIGINAL AS INSTRUMENT OF SERVICE, IS AND SHALL REMAIN THE PROPERTY OF ARNOLD C. ARCE & ASSOCIATES, REGISTERED ARCHITECT AND SUCH MUST NOT BE REPRODUCED OR COPIED IN PART OR IN WHOLE WITHOUT THEIR PERMISSION. ALL DRAWINGS ARE TO BE RETURNED WHEN NO LONGER IN USE.	DRAWN BY: DIANE FAYE P. PARAJES (POSITION)	PROJECT TITLE & LOCATION: PROPOSED PARSU TISSUE CULTURE BUILDING — PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	SUBMITTED BY: FELIPE B. PRIMAVERA, CE (DIRECTOR, PHYSICAL PLANT AND FACILITIES)	NOTED BY: JOEL P. SADOL (DEAN, SALOGON CAMPUS)	RECOMMENDING APPROVAL: ARNEL B. ZARCEDO, EDEL (VICE PRESIDENT FOR ADMINISTRATION & FINANCE)	APPROVED: RAUL S. BRADECINA, Ph.D. (SUC PRESIDENT II)	SHEET NO.: 03 / A–4

OFFICE OF THE PHYSICAL PLANT & FACILITIES

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

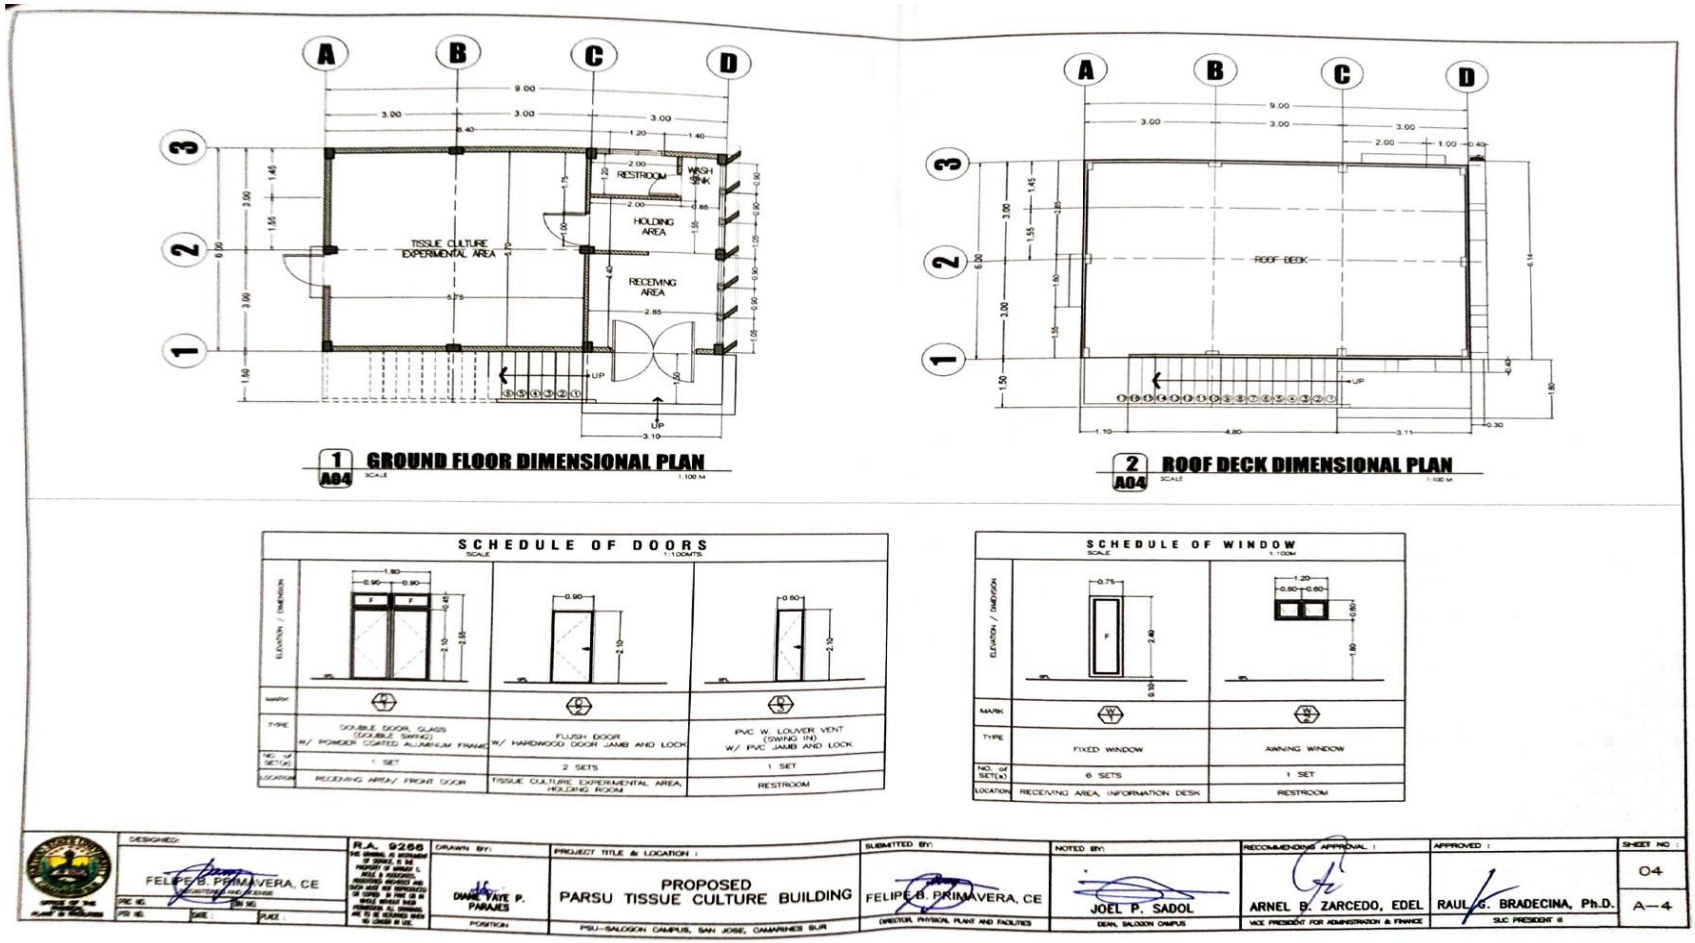

DESIGNED: FELIPE B. PRIMAVERA, CE	R.A. 9266	DRAWN BY: DIANE KATE P. PARAJES (POSITION)	PROJECT TITLE & LOCATION: PROPOSED PARSU TISSUE CULTURE BUILDING — PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	SUBMITTED BY: FELIPE B. PRIMAVERA, CE (DIRECTOR, PHYSICAL PLANT AND FACILITIES)	NOTED BY: JOEL P. SADOL (DEAN, SALOGON CAMPUS)	RECOMMENDING APPROVAL: ARNEL B. ZARCEDO, EDEL (VICE PRESIDENT FOR ADMINISTRATION & FINANCE)	APPROVED: RAUL G. BRADECINA, Ph.D. (SUC PRESIDENT III)	SHEET NO.: 04 A–4

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS


Masaganang Agrikultura, Maunlad na Ekonomiya

SCHEDULE OF BEAM


BEAM MARK	BEAM SECTION WIDTH	BEAM SECTION DEPTH	LEFT SUPPORT	MIDSPAN	RIGHT SUPPORT	STIRRUPS BAR SIZE	STIRRUPS SPACING	
B-1	200	400	5-16mmø G-40 3-16mmø G-40	3-16mmø G-40 5-16mmø G-40	5-16mmø G-40 3-16mmø G-40	10mmø	4 8 REST	50mm 100mm 175mm
B-2	250	500	5-16mmø G-40 3-16mmø G-40	3-16mmø G-40 5-16mmø G-40	5-16mmø G-40 3-16mmø G-40	10mmø	4 8 REST	50mm 100mm 175mm
B-3	200	300	4-16mmø G-40 2-16mmø G-40	2-16mmø G-40 4-16mmø G-40	4-16mmø G-40 2-16mmø G-40	10mmø	4 8 REST	50mm 100mm 175mm

SCHEDULE OF COLUMN


COLUMN ID MARK (X x Y)	FOUNDATION TO GROUND FLOOR	TOTAL NUMBER OF COLUMNS	STIRRUPS BAR SIZE	STIRRUPS SPACING	
C1 (200x 350)	10-16mm ø G-40	11	10mmø	4 8 REST	50mm 100mm 175mm



2 S01 DETAILED SECTION OF BEAM
SCALE 1:50 M

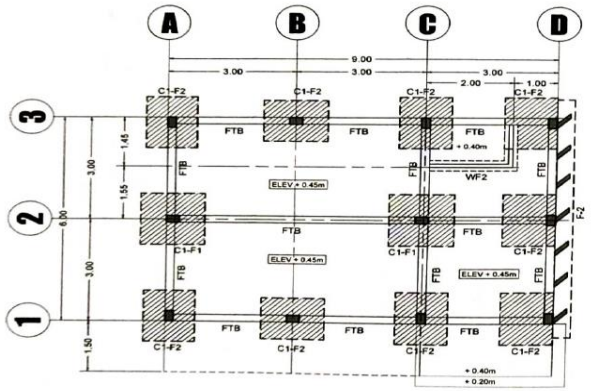

1 S01 FOUNDATION PLAN
SCALE 1:100 M

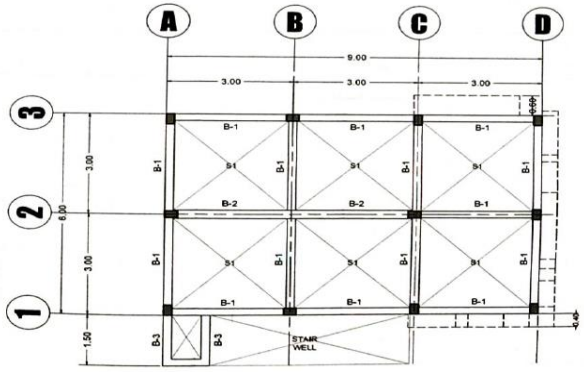


2 S01 FRAMING PLAN
SCALE 1:100 M

DESIGNED:	R.A. 9266	DRAWN BY:	PROJECT TITLE & LOCATION :	SUBMITTED BY:	NOTED BY:	RECOMMENDING APPROVAL :	APPROVED :	SHEET NO :
ENGR. FELIPE B. PRIMAVERA, CE PRC NO. / TIN NO. PTR NO. / DATE : / PLACE :	THE DRAWING AS INSTRUMENT OF SERVICE IS THE PROPERTY OF ARALOS C. MOLE & ASSOCIATES REGARDLESS ANYBODY SHALL NOT BE REPRODUCED OR COPIED IN PART OR IN WHOLE WITHOUT PRIOR PERMISSION. ALL DRAWINGS ARE TO BE RETURNED WHEN NO LONGER IN USE.	DIANNE FAYE P. PARAMES POSITION	PROPOSED PARSU TISSUE CULTURE BUILDING PSU-SALCOGON CAMPUS, SAN JOSE, CAMARINES SUR	FELIPE B. PRIMAVERA, CE DIRECTOR, PHYSICAL PLANT AND FACILITIES	JOEL P. SADOL DEAN, SALCOGON CAMPUS	ARNEL B. ZARCEDO, EDEL VICE PRESIDENT FOR ADMINISTRATION & FINANCE	RAUL G. BRADECINA, Ph.D. SUC PRESIDENT III	01 S-4

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS


Masaganang Agrikultura, Maunlad na Ekonomiya

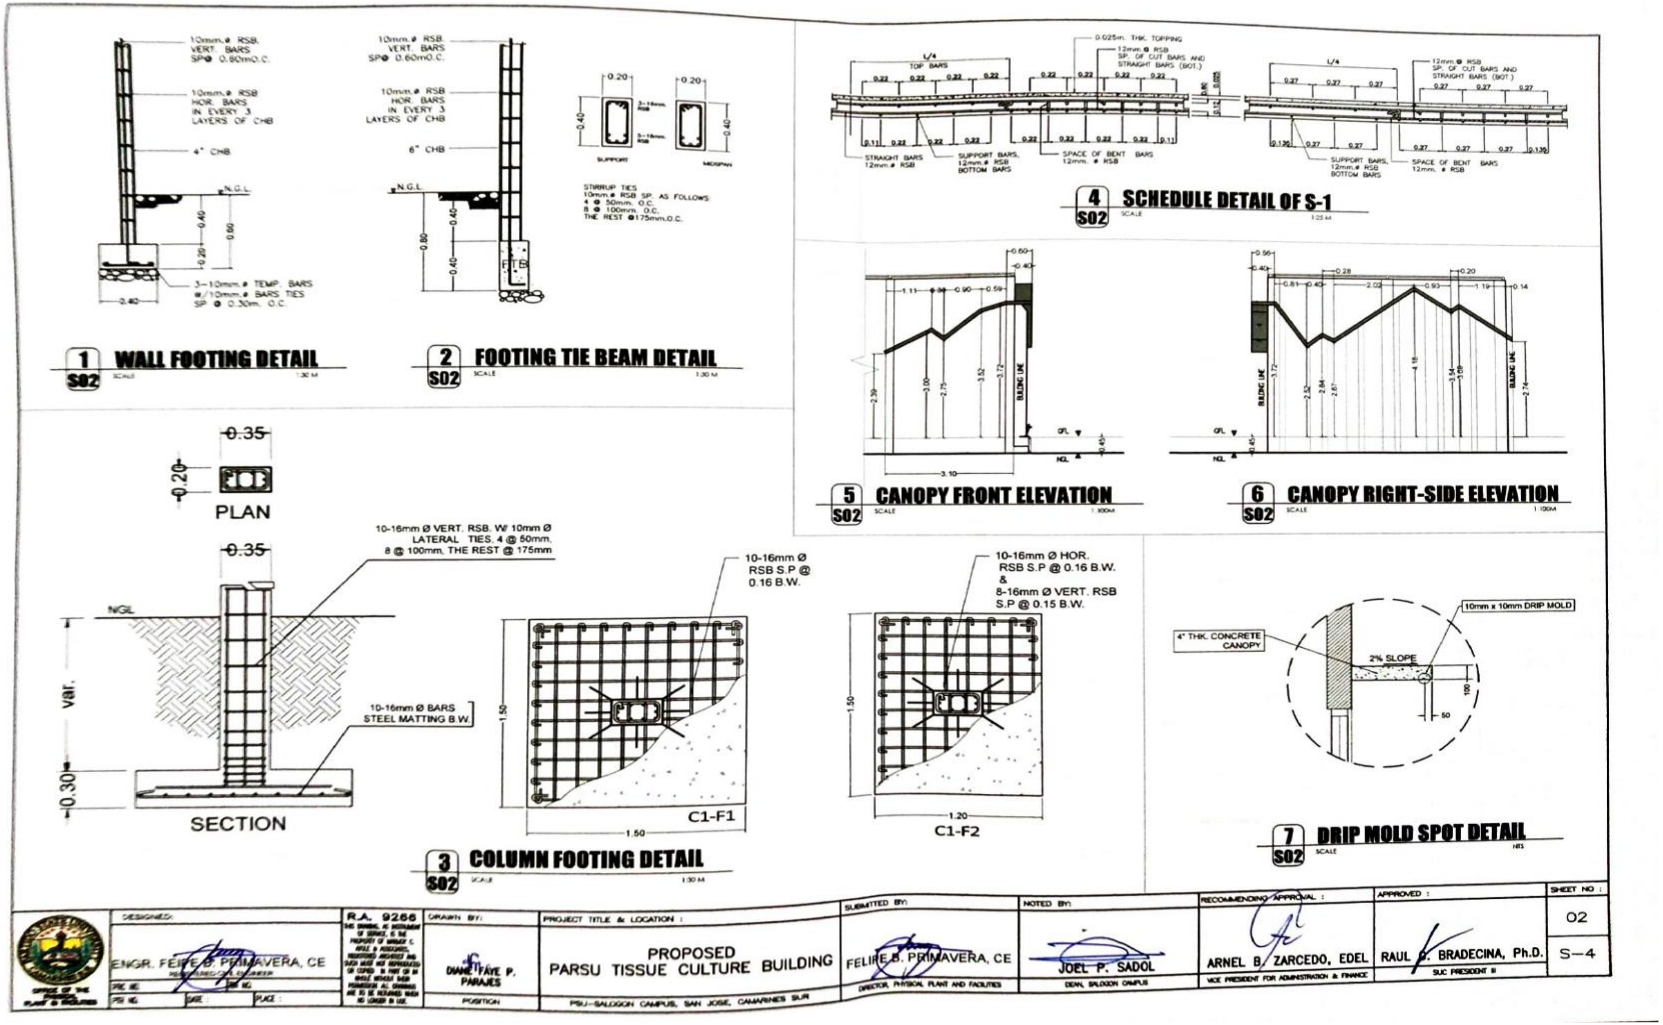

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

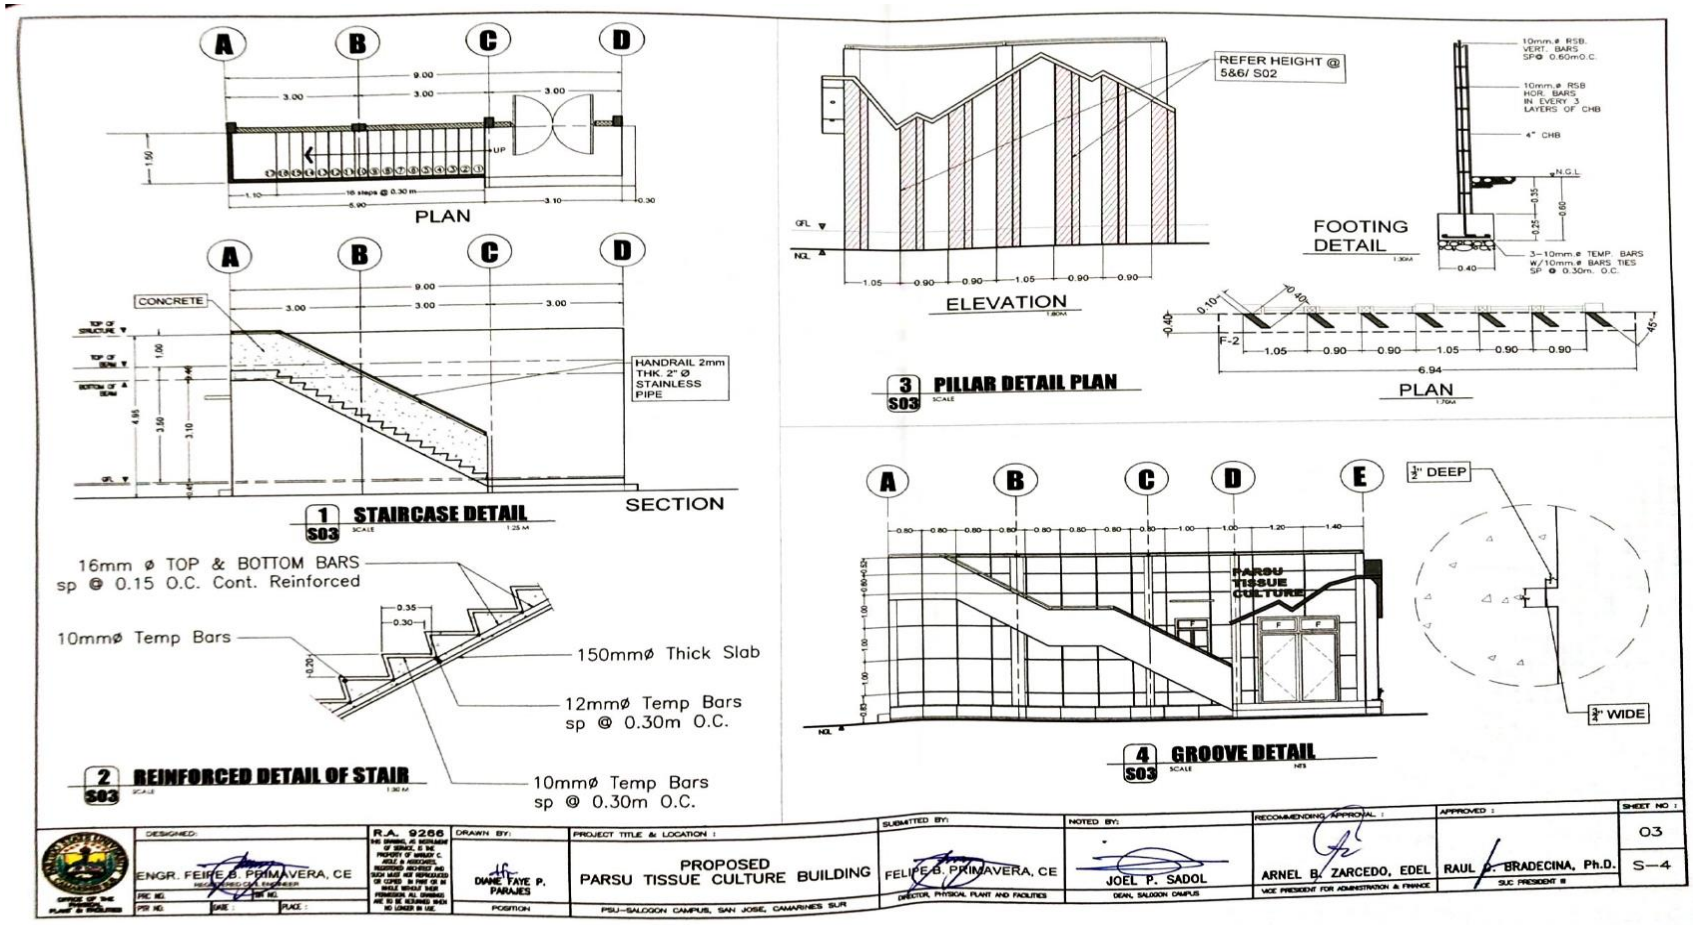


DESIGNED: ENGR. FELIPE B. PRIMAVERA, CE	R.A. 9266	DRAWN BY: DIANE FAYE P. PARAJES	PROJECT TITLE & LOCATION: PROPOSED PARSU TISSUE CULTURE BUILDING, PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	SUBMITTED BY: FELIPE B. PRIMAVERA, CE, DIRECTOR, PHYSICAL PLANT AND FACILITIES	NOTED BY: JOEL P. SADOL, DEAN, SALOGON CAMPUS	RECOMMENDING APPROVAL: ARNEL B. ZARCEDO, EDEL, VICE PRESIDENT FOR ADMINISTRATION & FINANCE	APPROVED: RAUL D. BRADECINA, Ph.D., SUC PRESIDENT III	SHEET NO.: 03 / S–4


REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS


Masaganang Agrikultura, Maunlad na Ekonomiya

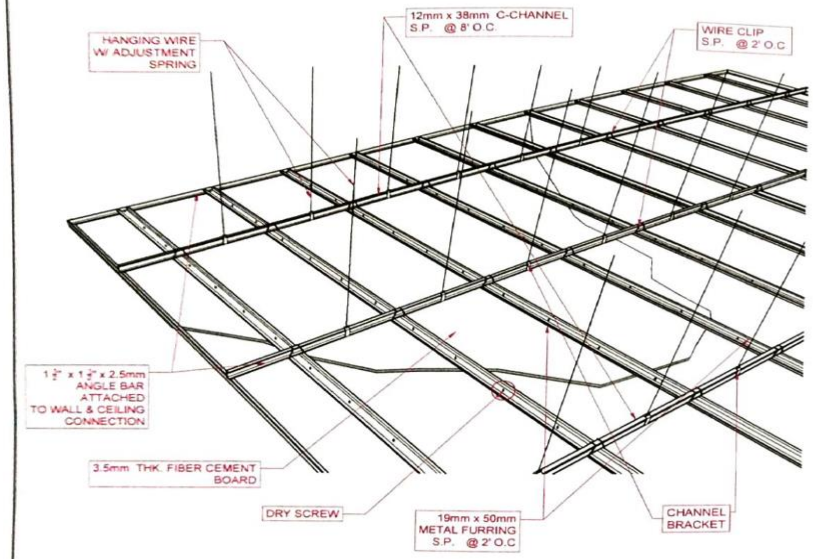


4 S03 CEILING DETAIL
SCALE NTS



SECTION

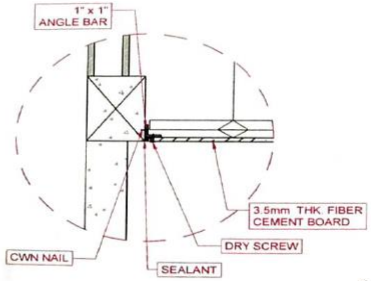

DETAIL A

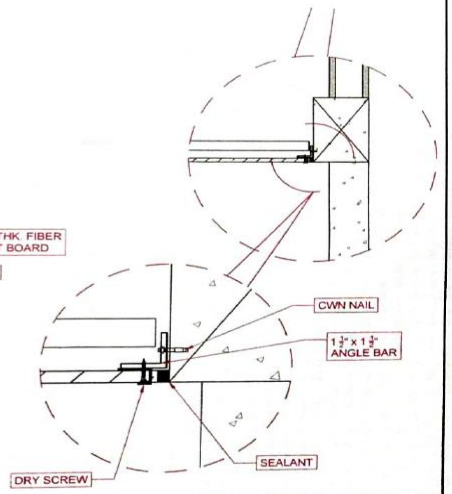

DESIGNED:	R.A. 9266	DRAWN BY:	PROJECT TITLE & LOCATION :	SUBMITTED BY:	NOTED BY:	RECOMMENDING APPROVAL :	APPROVED :	SHEET NO :
ENGR. FELIPE B. PRIMAVERA, CE REGISTERED ENGINEER PRC NO. / TIN NO. PTR NO. / DATE: / PLACE:	THE DRAWING AS INSTRUMENT OF SERVICE, IS THE PROPERTY OF WINSLEY C. REGO & ASSOCIATES, REGISTERED ARCHITECT AND SUCH MAY NOT BE REPRODUCED OR COPIED IN PART OR IN WHOLE WITHOUT HER PERMISSION. ALL DRAWINGS ARE TO BE RETURNED WHEN NO LONGER IN USE.	DIANE FAYE P. PARAJES POSITION	PROPOSED PARSU TISSUE CULTURE BUILDING PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	FELIPE B. PRIMAVERA, CE DIRECTOR, PHYSICAL PLANT AND FACILITIES	JOEL P. SADOL DEAN, SALOGON CAMPUS	ARNEL B. ZARCEDO, EDEL VICE PRESIDENT FOR ADMINISTRATION & FINANCE	RAUL G. BRADECINA, Ph.D. SUC PRESIDENT III	04 S–4

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

SPECIFICATIONS:

01. ALL ELECTRICAL WORKS SHALL BE DONE IN ACCORDANCE WITH THE RULES AND REGULATIONS OF THE LATEST EDITION OF THE PHILIPPINE ELECTRIC CODE, APPLICABLE ORDINANCES OF THE LOCAL GOVERNMENT AND WITH THE REQUIREMENTS OF THE LOCAL COMPANY POWER.
02. METALLIC ENCLOSURES, RACEWAY AND ELECTRICAL EQUIPMENT SHALL BE GROUNDED.
03. MINIMUM SIZE OF WIRE SHALL BE 2.0mm2 THHN AND THE MINIMUM SIZE OF CONDUIT SHALL BE 20mm DIAMETER, UNLESS OTHERWISE INDICATED IN THE PLAN.
04. WHEREVER REQUIRED AND NECESSARY, PULL BOXES AND JUNCTION BOXES OF PROPER SIZES SHALL BE INSTALLED AT CONVENIENT AND INCONPICUOUS LOCATIONS ALTHOUGH SUCH BOXES ARE NOT SHOWN ON THE PLANS NOR MENTIONED IN THE SPECIFICATIONS.
05. ALL LIGHTING CIRCUIT HOMERUNS AND CONVENIENCE OUTLETS SHALL BE WIRED WITH NO LESS THAN 3.5mm2 THHN IN SIZE. ALL 20 AMPERE CIRCUIT HOMERUN TO PANEL BOARD MORE THAN 30 METERS IN LENGTH SHALL BE WIRED WITH NO LESS THAN 5.5mm2 THHN, UNLESS OTHERWISE INDICATED ON THE PLAN.
06. THE CONTRACTOR SHALL VERIFY AND ORIENT THE ACTUAL LOCATION OF SERVICE ENTRANCE FOR CONNECTION TO POWER LOCAL COMPANY SERVICE POINT.
07. ALL WIRING SHALL BE INSTALLED IN STANDARD MOLDFLEX OR PVC ELECTRICAL CONDUITS. RUN EMBEDDED INSIDE THE CONCRETE AND THE HOLLOW BLOCKS STRUCTURES, SLABS, COLUMNS, WALLS, PARTITIONS AND INSIDE THE CEILING SPACES, WHERE THE USE OF CONCEALED CONDUIT WIRING IS IMPRACTICABLE SURFACE METAL, PVC MOLDING MAY BE USED.
08. ELECTRICAL WORKS SHALL BE DONE UNDER THE DIRECT AND FULL SUPERVISION OF A DULY LISENCED ELECTRICAL ENGINEER OR REGISTERED MASTER ELECTRICIAN.
09. PANEL BOARD SHALL BE COMPLETE WITH BUS, ENCLOSURE AND TRIM, COMPLETE AND MOLDED CASE CIRCUIT BREAKER, WITH RATING AS INDICATED. PROVIDE A TYPED CIRCUIT DIRECTORY.
10. ALL ELECTRICAL DEVICES AND EQUIPMENT EXPOSED TO WEATHER SHALL BE WEATHERPROOF.
11. ELECTRICAL SERVICE FOR THE PREMISES SHALL BE 230V, 1 PHASE, 2 WIRE.
12. COORDINATE WITH MECHANICAL CONTRACTOR FOR EQUIPMENT REQUIREMENTS AND PROVIDE ALL WIRING EQUIPMENT REQUIRED.
13. TEST: THE FOLLOWING SHALL BE TESTED IN PRESENCE OF ENGINEER, AND RESULTS SUBMITTED TO ENGINEER FOR APPROVAL.
    A. OPERATION TEST
    B. INSULATION RESISTANCE
    C. GROUND RESISTANCE (IF THERE IS GROUD ROD)
14. THE DRAWINGS AND SPECIFICATIONS ARE MEANT TO BE COMPLIMENTARY TO EACH OTHER AND WHAT IS REQUIRED BY ONE SHALL BE BINDING IF CALLED BY BOOTH. ANY APPARENT CONFLICT BETWEEN THE DRAWINGS AND SPICIFICATIONS, AND ANY CONTROVERSIES OR UNCLEAR POINTS IN EITHER, SHALL BE REFERED TO ELECTRICAL CONSULTANTS OR DESIGNER FOR THE FINAL DESIGN.
15. ALL REVISION OR ADDITIONAL WORKS ON ELECTRICAL PLANS SHOULD CONSULTED TO THE DESIGNER (P.E.E.).


PB

LOAD SCHEDULE AND DESIGN COMPUTATION


CKT No.	LOAD DESCRIPTION	QTY	S1	S2	S3	3WAY	VOLTS	VA	AMPERE	SIZE / TYPE OF WIRE	SIZE / TYPE OF CONDUIT	C.B. RATING	
1	LIGHTING OUTLET	8	2	3			230	800	3.48	2c - 2.0mm2 THHN 1c - 2.0mm2 THHN	20 mm Ø uPVC	15 AT, 2P	AFCI
2	LIGHTING OUTLET	5	1				230	500	2.17	2c - 2.0mm2 THHN 1c - 2.0mm2 THHN	20 mm Ø uPVC	15 AT, 2P	AFCI
3	CEILING FAN	2	1	1			230	200	0.87	2c - 2.0mm2 THHN 1c - 2.0mm2 THHN	20 mm Ø uPVC	15 AT, 2P	AFCI
4	CONVENIENCE OUTLET	10					230	1800	7.83	2c - 3.5mm2 THHN 1c - 3.5mm2 THHN	20 mm Ø uPVC	20 AT, 2P	GFCI
	TOTAL							3,300 VA	14.33 AMP.				

MAIN CB=

MAIN FEEDER=

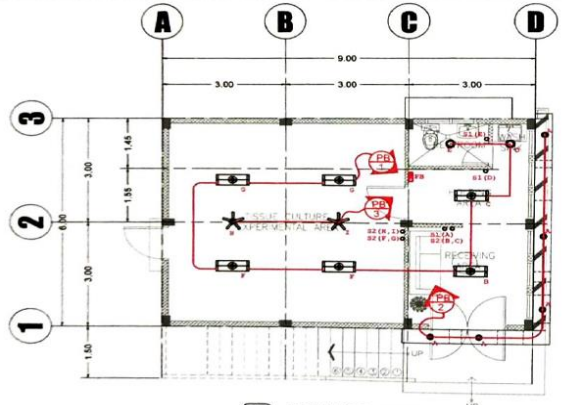

1 E01 **LIGHTING LAYOUT** SCALE 1:100 M

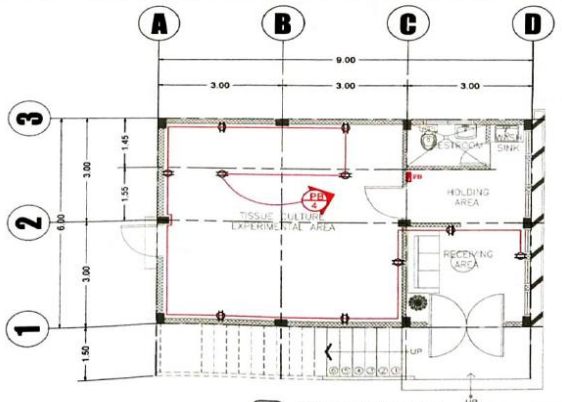

2 E01 **POWER LAYOUT** SCALE 1:100 M

ELECTRICAL LEGEND:


SYMBOL	DESCRIPTION
	LED BULB
	LED TUBE LIGHT ON LOUVER HOUSING
	PINLIGHT
	CEILING FAN
S1	SINGLE POLE SWITCH
S2	TWO GANG SWITCH
S3	THREE GANG SWITCH
PB	PANEL BOARD
	CIRCUIT HOMERUN
	TRIPLEX RECEPTACLE OUTLET
	DUPLEX RECEPTACLE OUTLET
	ACU
	CONVENIENCE CIRCUIT LINE
	LIGHTING CIRCUIT LINE

DESIGNED:	DRAWN BY:	PROJECT TITLE & LOCATION :	SUBMITTED BY:	NOTED BY:	RECOMMENDING APPROVAL :	APPROVED :	SHEET NO :
REGISTERED ELECTRICAL ENGINEER PRC NO. / TIN NO. PTR NO. / DATE / PLACE	R.A. 9266 DIANE FAYE P. PARAJES POSITION	PROPOSED PARSU TISSUE CULTURE BUILDING PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	FELIPE B. PRIMAVERA, CE DIRECTOR, PHYSICAL PLANT AND FACILITIES	JOEL P. SADOL DEAN, SALOGON CAMPUS	ARNEL B. ZARCEDO, EDEL VICE PRESIDENT FOR ADMINISTRATION & FINANCE	RAUL B. BRADECINA, Ph.D. SUC PRESIDENT III	1 E–1


REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya



PLAN

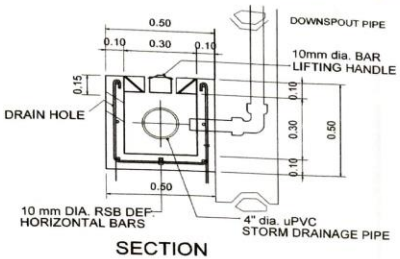


SECTION

3 P01 CATCH BASIN DETAIL
SCALE NTS


LEGEND :

	WASTE PIPE LINE
	SEWER PIPE LINE
	DOWNSPOUT
	WATER SUPPLY LINE
M	WATER METER
CB	CATCH BASIN
WC	WATER CLOSET
LAV	LAVATORY
CO	CLEAN OUT
FD	FLOOR DRAIN

LC	LEACHING CHAMBER
MH	MANHOLE
CV	CHECK VALVE
PPR	POLYPROPYLENE RANDOM COPOLYMER
uPVC	UNPLASTICIZED POLYVINYL CHLORIDE
VSTR	VENT STACK THRU ROOF
CO	CLEAN OUT
GV	GATE VALVE
UR	URINAL
KS	KITCHEN SINK

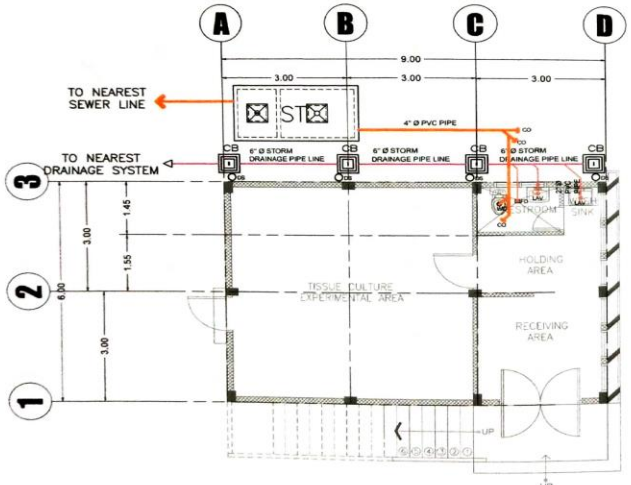

1 P01 GROUND FLOOR SEWER LINE LAYOUT
SCALE 1:100 M

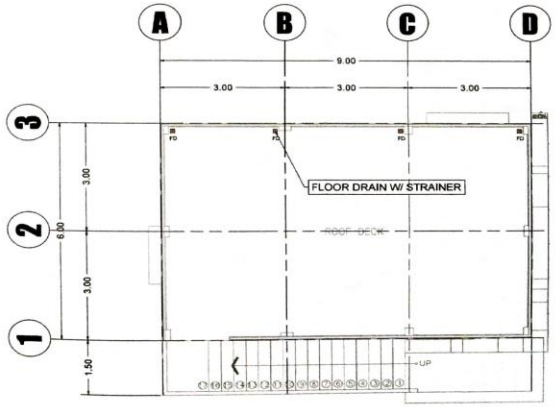


2 P01 ROOF DECK SEWER LINE LAYOUT
SCALE 1:100 M

DESIGNED: MARJORIE C. ATOLE, SANITARY ENGINEER	R.A. 9266	DRAWN BY: DIANE FAYE P. PARAJES, POSITION	PROJECT TITLE & LOCATION: PROPOSED PARSU TISSUE CULTURE BUILDING, PSU–SALOGON CAMPUS, SAN JOSE, CAMARINES SUR	SUBMITTED BY: FELIPE B. PRIMAVERA, CE, DIRECTOR, PHYSICAL PLANT AND FACILITIES	NOTED BY: JOEL P. SADOL, DEAN, SALOGON CAMPUS	RECOMMENDING APPROVAL: ARNEL B. ZARCEDO, EDEL, VICE PRESIDENT FOR ADMINISTRATION & FINANCE	APPROVED: RAUL B. BRADECINA, Ph.D., SUC PRESIDENT III	SHEET NO.: 01 P–3

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

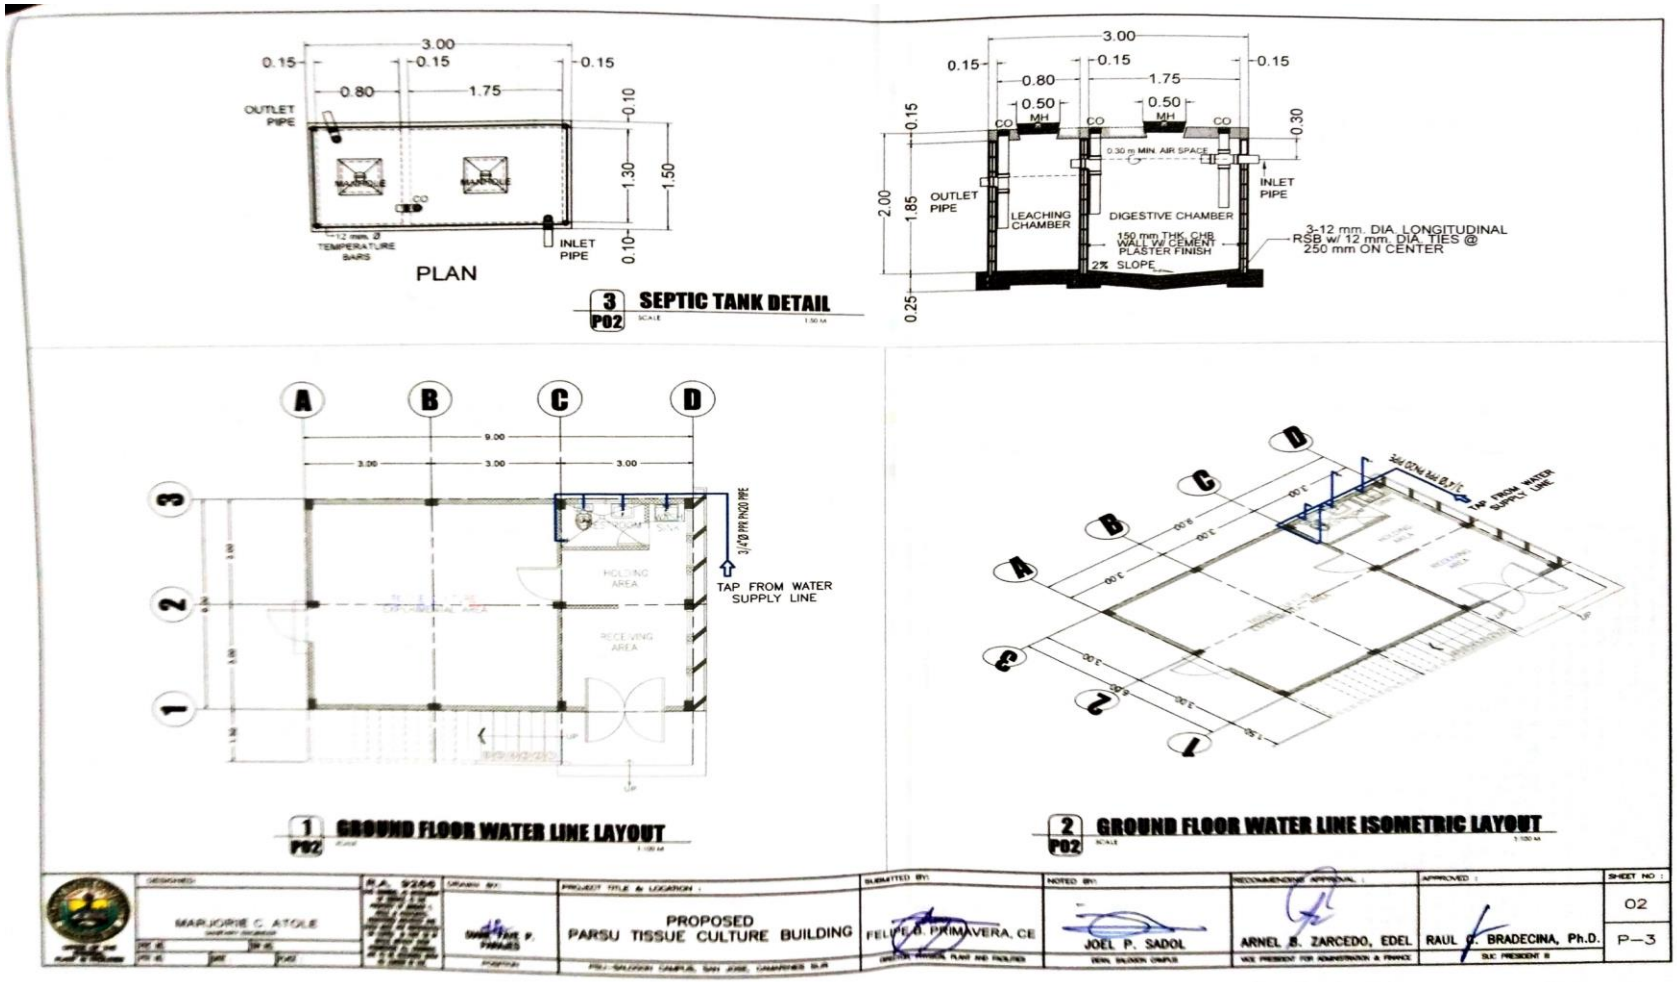

3 P02 **SEPTIC TANK DETAIL**

1 P02 **GROUND FLOOR WATER LINE LAYOUT**


2 P02 **GROUND FLOOR WATER LINE ISOMETRIC LAYOUT**

DESIGNED: MARJORIE C. ATOLE	R.A. 9266	DRAWN BY:	PROJECT TITLE & LOCATION: PROPOSED PARSU TISSUE CULTURE BUILDING	SUBMITTED BY: FELIPE O. PRIMAVERA, CE	NOTED BY: JOEL P. SADOL	RECOMMENDING APPROVAL: ARNEL B. ZARCEDO, EDEL	APPROVED: RAUL D. BRADECINA, Ph.D.	SHEET NO.: 02 / P–3

REPUBLIC OF THE PHILIPPINES
DEPARTMENT OF AGRICULTURE
BUREAU OF AGRICULTURAL RESEARCH
RDMIC Bldg., Elliptical Road corner Visayas Avenue, Diliman, Quezon City 1104
(+632) 8461 2800 and (+632) 8461 2900 • r4d@bar.gov.ph

BAGONG PILIPINAS

Masaganang Agrikultura, Maunlad na Ekonomiya

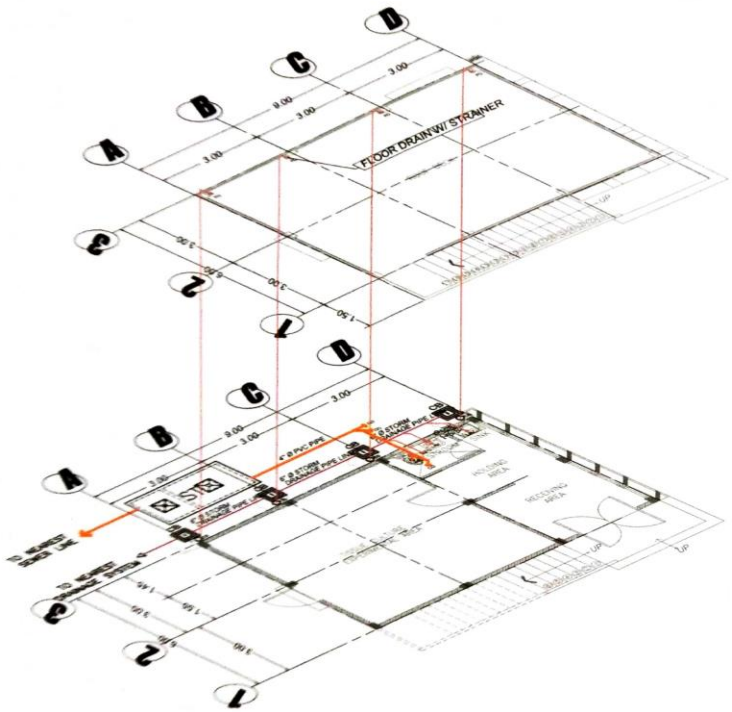

1 P03 **SEWER LINE ISOMETRIC LAYOUT**

SPECIFICATIONS:

ALL PLUMBING WORKS SHALL BE DONE IN ACCORDANCE WITH THE LATEST PROVISION OF THE NATINAL CODE OF THE REQUIREMENTS OF THE LOCAL PLUMBING CODE INSPECTION OFFICE AND PERTINENT PROVISIONS OF THE EXISTING BUILDING CODE.

RUN ALL HORIZONTAL PIPINGS IN PERFECT ALIGNMENT AT A UNIFORM GRADE OF NOT LESS THAN TWO PERCENT.

ALL CHANGE DIRECTION SHALL BE MADE BY APPROPRIATE USE OF FOURTY-FIVE DEGREES (45) WYE, LONG SWEEP QUARTER BEND SIXTH-EIGHT OR SEVENTENTH - BENDS WHEN THE CHANGE OF FLOW IS HORIZONTAL SOIL OR WASTE LINES, TEE & CROSSES MAY BE USED ON VENT PIPE.

NO DOUBLE HUB OR TEE BRANCH SHALL BE USED ON HORIZONTAL SOIL OR WASTE LINES, THE DRILLING, THE TAPPING ON HORIZONTAL SOIL OR VENT PIPES & USED OF DOUBLE HUB & BENDS ARE PROHIBITED.

PROVIDE PIPE SLEEVES AT WALL SLAB STONE SIZE BIGGER THAN THE ACTUAL LINES PASSING THROUGH WALLS OR UNDER SLAB TO PROTECT PIPE FROM BREAKAGE.

THE DIGESTION CHAMBER OF SEPTIC VAULT MUST BE WATER PROOFED.

NOT LESS THAN 300 mm OF AIR SPACE MUST MUST BE LEFT BETWEEN TOP OF THE SEWAGE AND THE UNDER PART OF THE VAULT ROOF SLAB.

NO SEPTIC VAULT SHALL BE CONSTRUCTED UNDER THE BUILDING.

ALL PLUMBING WORKS SHALL BE UNDER THE DIRECT SUPERVISION OF LICENSED SANITARY ENGINEER OR MASTER PLUMBER.

DESIGNED:	R.A. 9266	DRAWN BY:	PROJECT TITLE & LOCATION:	SUBMITTED BY:	NOTED BY:	RECOMMENDING APPROVAL:	APPROVED:	SHEET NO.:
MARJORIE C. ATOLE			PROPOSED PARSU TISSUE CULTURE BUILDING	FELIPE B. PRIMAVERA, CE	JOEL P. SADOL	ARNEL B. ZARCEDO, EDEL	RAUL C. BRADECINA, Ph.D.	3
			PSU-SALCEDO CAMPUS, SAN JOSE, CAMARINES SUR					P-3
